



City of Austin

Site Plan Application – Master Comment Report

This Master Comment Report includes all staff comments received to date about your most recent site plan submittal. The comments may include requirements, recommendations, or information. The requirements in this report must be addressed by an updated site plan submittal.

Case Number: SP-2026-0136C

Revision #: 00

Case Manager: Jim Gobel

Phone #: (512) 978-6414

Update: U0

Email : Jim.Gobel@austintexas.gov

Project Name: 1700 South Lamar

Location: 1700 S LAMAR BLVD

Submittal Date: May 18, 2026

Report Due Date: June 7, 2026

Final Report Date: June 8, 2026

1 DAY HAS BEEN ADDED TO THE UPDATE DEADLINE

Update Deadline (Expiration Date): May 19, 2027

Final Update Deadline [LDC § 25-5-113]:

- **Failure to submit a final update by the deadline will result in the automatic denial of the application, unless:**
 - (1) The site plan application has been approved; or
 - (2) A request for an extension has been granted. [LDC § 25-1-82(F)]
- If the deadline falls on a weekend or [City of Austin holiday](#), the next City of Austin workday will be the deadline.
- The applicant or their agent is responsible for updating this site plan application and clearing all comments.

Update Submittals:

- **A formal update submittal is required.** Updates can be submitted through the [Site Plan Update and Formal Web Form](#). Updates submitted after 3:00 p.m. may be processed on the following business day.
- A written response to every comment is required in addition to the updated plan set.
- More comments may be generated as a result of information or design changes provided in your update.

Site Plan Approval:

- The site plan will be approved when all requirements from each review discipline have been addressed.

REVIEWERS:

Electric: Rosemary Avila
TPW-TDS: Bryan Golden
Drainage Engineering: Connor Flanagan
City Arborist: Dillon Olsen
Environmental: Kymberli Herron
Fire For Site Plan: Constantino Mendoza
Land Development Engineering: William Bennett
Industrial Waste: Jonathan Bode
PARD / Planning & Design: Kathleen Stanford
Site Plan: Randall Rouda

Site Plan Plumbing: Cory Harmon
ATPW Utility Coordination: John Carr
Traffic Control: Traffic Control Review
AW Utility Development Services: Bradley Barron
Water Quality: Connor Flanagan
AW Pipeline Engineering: David Lara
AW Reclaim and Reuse: Dalila Loiacomo
AW OWB Review: Natalie Ortiz
Case Manager: Jim Gobel

Electric Review – Rosemary Avila (512) 972-8488 - rosemary.avila@austinenergy.com

See BlueBeam link below to download AE site comments:

Link: [https://studio.bluebeam.com/share/\\$ZU5vWkV5UnFhdTB](https://studio.bluebeam.com/share/$ZU5vWkV5UnFhdTB)

Applicant, for your comment responses use the color BLUE.

Site Plan Preliminary Design Requirements

Austin Energy Design Criteria Effective December 12th, 2023

•[UCM § 1.3.8 - Customer Electrical Facilities that Cross Property Lines](#)

•[UCM § 1.3.12 - AE Line Extension Policy](#)

•[UCM § 1.3.16- Truck Access to AE Construction and Existing Facility Sites](#)

•[UCM § 1.9.3 - Installation of Metering Equipment](#)

•[UCM § 1.10.3 - Permanent Clearances from AE Overhead Lines and Facilities](#)

•[UCM § 1.10.4 - Clearances from AE Padmount Equipment and Distribution Vaults](#)

•[UCM § 1.10.10.3 & 4 - Customer Activity in Utility Easements - Landscaping
& Trees](#)

•[Appendix F of the Environmental Criteria Manual](#)

TPW-TDS Review – Bryan Golden (512) 974-2426 - bryan.golden@austintexas.gov

TPW 1: Comment Status:

- Please add the following note to the coversheet: Development of structures that require a building permit within this Site Plan, or revisions thereof, are required to comply with the City of Austin Street Impact Fee Ordinances, as applicable, and must be paid upon completion of the building permit plan review for each building.
Reference: LDC 25-6-662

TPW 2: Comment Status:

- The Building Permits for this site are required to comply with the City's Street Impact Fee. The fee was adopted by City Council in December 2020 and is applicable to all Building Permits submitted on or

after June 22, 2022. (For more information: <https://www.austintexas.gov/department/street-impact-fee>). Please complete a copy of the SIF worksheet: <https://atd.knack.com/development-services#customer-portal/services/street-impact-fee-worksheet/> This development may be eligible for SIF offsets if off-site transportation mitigations are included with the site plan. Please inform this reviewer if you would like these options pursued.

Reference: LDC 25-6-662

TPW 3: Comment Status:

- The ASMP requires 116 of right-of-way for S. Lamar. Verify existing ROW is sufficient with a survey tie or dedicate 58 feet of right-of-way from the existing centerline in accordance with the ASMP.

Reference: LDC 25-6-55

TPW 4: Comment Status:

- Right-of-way (ROW) dedication requirement is subject to the maximum street-impact-fee (SIF), also known as Rough Proportionality (RP), as per LDC 25-6-662 & LDC 25-6-23. For the formal staff assessment of the SIF and ROW dedication, please complete and submit the SIF worksheet available at <https://atd.knack.com/development-services#services/street-impact-fee-worksheet/>.

Reference: LDC 25-6-55

TPW 5: Comment Status:

- An administrative waiver may be requested for <insert code>. For a formal staff assessment of the waiver request, please complete and submit the worksheet available at <https://atd.knack.com/development-services#customer-portal/services/tpw-waiver/>. Please note a waiver review fee will be assessed.

Reference: LDC 25-6, TCM 10.2.1

TPW 6: Comment Status:

- On-street parking is prohibited within 15 ft of either side of fire hydrants. *Dimension the distance between the on-street parking and the fire hydrant.*

Reference: TCM 9.2.3.1.B. TCM Figure 9-2.

TPW 7: Comment Status:

- The nearest edge of an on-street parking stall shall be a minimum of 30 feet from the curbside of a crosswalk and a minimum of 30 feet from the approach to an intersection (this does not include driveways).

Reference: TCM 9.2.3.1.C, D.


TPW 8: Comment Status:

- Concrete pavement is required for on-street parking. Any such pavement must comply with TCM Section 14 Pavement Design.

Reference: TCM 9.2.0.C., 2.8.2.2


TPW 9: Comment Status:

- Parking bulb-outs must adhere to standard design (see below).
Reference: TCM Fig. 9-2, 9.2.3.1

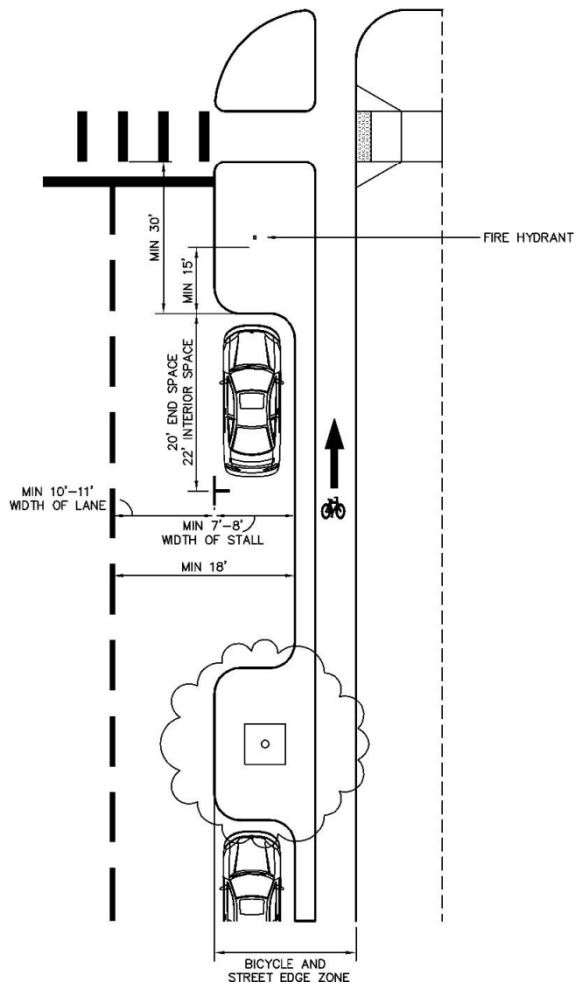

TPW 10: Comment Status:

- Use one of the standards from SD 440-2 for bike lane transition from Collier Street to protected intersection. *Tactile indicators, directional markings and warning surfaces are needed. Where bike ramp and sidewalk merge, scramble area should be 8' min.*
Reference: TCM 5.2.0.

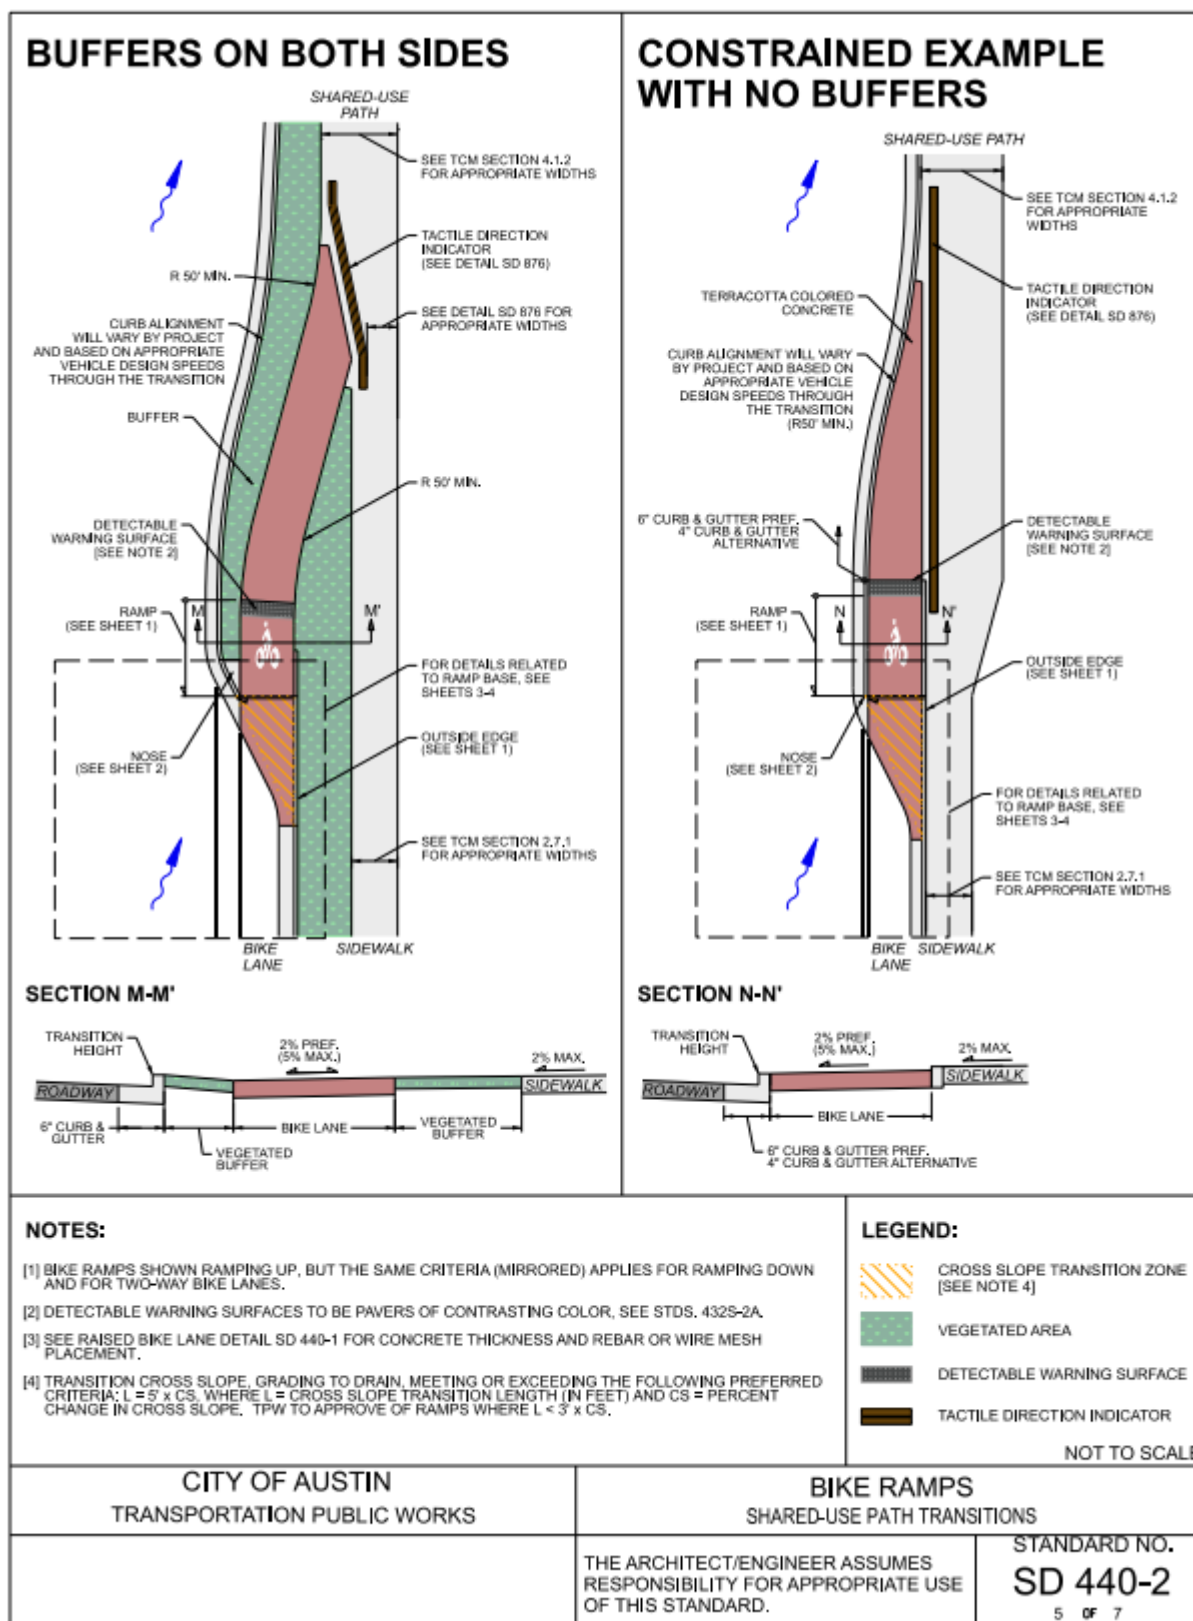


TPW 11: Comment Status:

- Please add the following note to site plan if on-street parking is proposed "None of the on-street spaces are reserved for the development and may be used by any member of the public. The developer must

be aware that they can count on-street spaces at their own risk; the spaces may be removed at any time for any reason and the City of Austin will not relocate displaced on-street parking. In addition, if the adjoining street applies for and receives Residential Permit Parking, the parking for the development will not count as residential parking and the residents will not receive Residential Parking Permits.”
Reference: TCM, 9.2.0.B.

TPW 12: Comment Status:

Collier Streetscape: A 7' tree and furniture (planting) zone, measured from the back of curb is required. *Street trees placed 30' on center are required.* A license agreement may be required. This is to be followed by a 5' minimum clear zone (sidewalk) and a min. 2' buffer zone between the building/property line. *TCM 2.8.2.2*

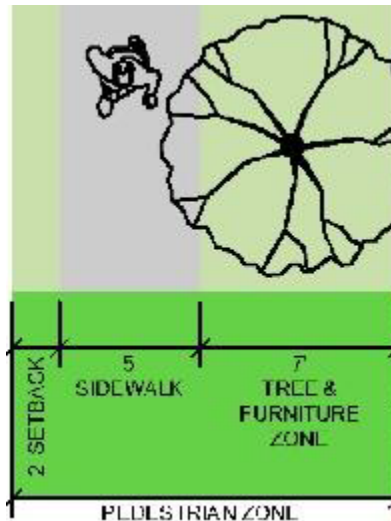

TPW 13: Comment Status:

- S. Lamar Street Edge: A 2' buffer zone, measured from the proposed back of curb, is required. This is to be followed by a minimum 7' bike lane. **Call out integral terra cotta color (spec SP360S).** *TCM Table 2-2.*
- S. Lamar Streetscape: A minimum 8' tree and furniture (planting) zone, measured from proposed back of curb is required. *Street trees placed 30' on center are required.* A license agreement may be required. This is to be followed by a 6' minimum clear zone (sidewalk) and a min. 1' buffer zone between the building/property line. *TCM Table 2-2; TCM 11.2.2.1.B, TCM 4.1.1.J*
- An administrative waiver may be requested for the elements required under TCM Table 2-2. *A 10' SUP (with integrated terra cotta color) may be utilized instead of split facilities.* For a formal staff assessment of the waiver request, please complete and submit the worksheet available at <https://atd.knack.com/development-services#customer-portal/services/tpw-waiver/>. Please note a waiver review fee will be assessed.
Reference: LDC 25-6, TCM 10.2.1

TPW 14: Comment Status:

- Where required, the sidewalk shall extend onto private property to fulfill the minimum requirement, with a sidewalk easement provided. *Provide an additional two feet within the easement for maintenance purposes.*


Reference: LDC 25-2 Subchapter E (§2.2.2.B) and TCM, 4.1.1, 4.1.2.

TPW 15: Comment Status:

- When pedestrian and bicycle facilities are combined into a shared use path, the shared use path shall be located between the right-of-way line and Tree & Furniture Zone unless placement in an easement is approved by applicable staff.

Reference: TCM 4.1.2A

- A SUP configuration will be allowed (with waiver) if planted tree zone is located back-of-curb; roughly following this alignment:*

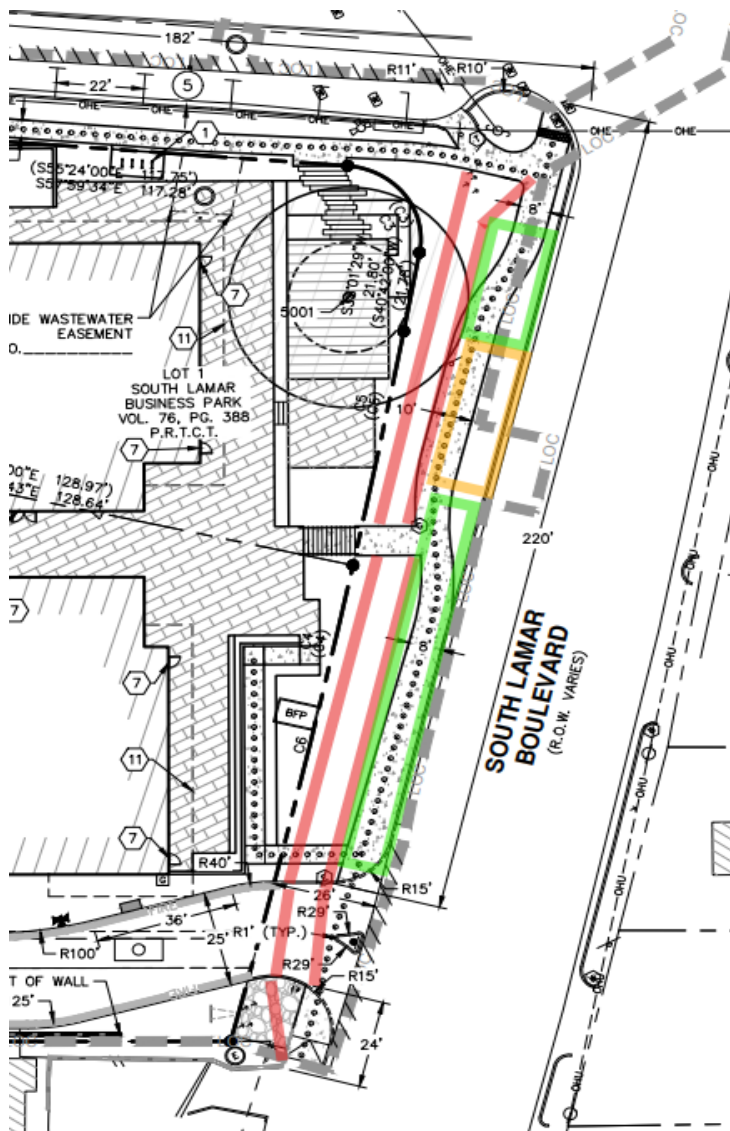


For future bus stop, please use the shared use path detail:


SHARED-USE PATH BEHIND BUS LANDING AREA

LEADING TRANSITION ZONE


TRAILING TRANSITION ZONE

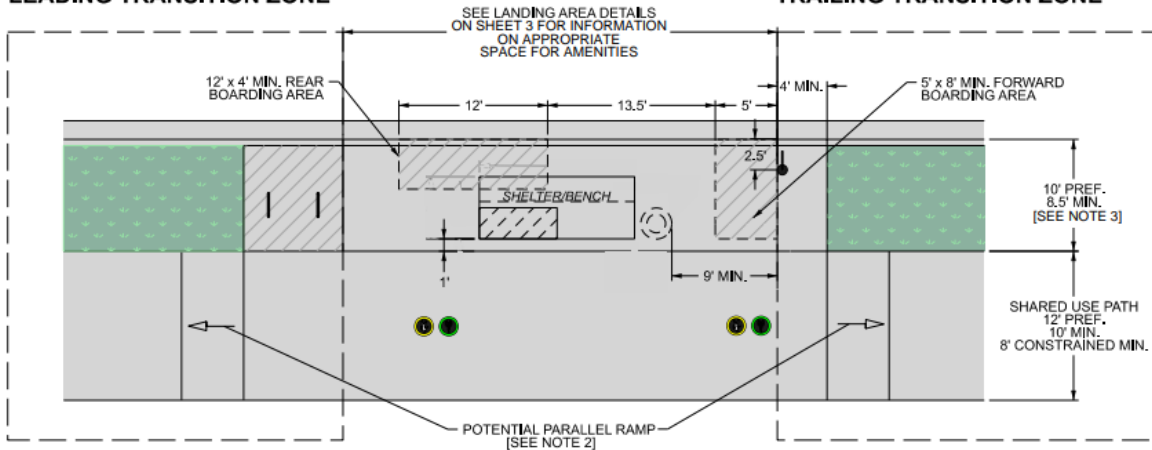

ALTERNATE LEADING TRANSITION

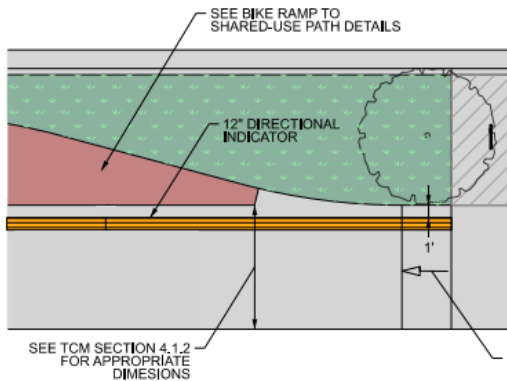

ALTERNATE TRAILING TRANSITION

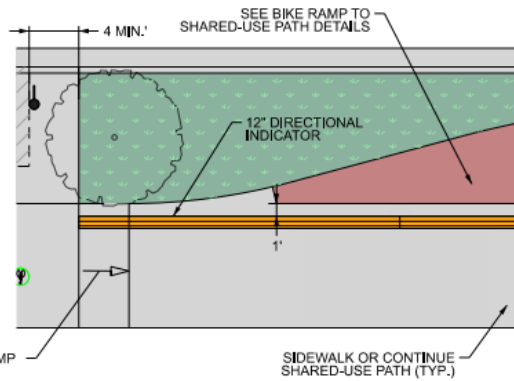

NOTES:

- [1] IF NO SHELTER IS PRESENT, ANY STREET FURNITURE PRESENT MUST ACCOMMODATE AT LEAST A 2' MIN. SHY DISTANCE FROM CURB FACE AND 1' MIN. SHY DISTANCE FROM THE EDGE OF THE PROTECTED BIKE LANE AND SHARED USE PATH.
- [2] PARALLEL RAMP MAY BE REQUIRED IN SHARED-USE PATH TO ACHIEVE ADA COMPLIANT CROSS SLOPS WHILE TRANSITIONING BETWEEN 6" AND 9" CURBS AT THE BUS STOP.
- [3] SEE CAPMETRO STRUCTURAL STANDARDS APPLICABLE TO SHELTER TYPE.
- [4] FOR SHARED USE PATH CONCRETE JOINTS, SEE STANDARDS 1302S-2 AND 1302S-3.

LEGEND:


- DIRECTIONAL INDICATOR (SEE DETAIL XX)
- STAMPED CONCRETE
- POTENTIAL VEGETATED AREA
- BUS FLAG POLE
- TRASH RECEPTACLE [SEE NOTE 5]
- POTENTIAL CLEAR AREA FOR BICYCLE (INCLUDING RACKS) OR MICROMOBILITY PARKING (SEE DETAIL XX)

NOT TO SCALE

CITY OF AUSTIN
AUSTIN TRANSPORTATION DEPARTMENT

BUS STOP
SHARED-USE PATH STOP BEHIND LANDING

- Note planned curb height is 9" for the bus stop pad per corridor improvements plans:

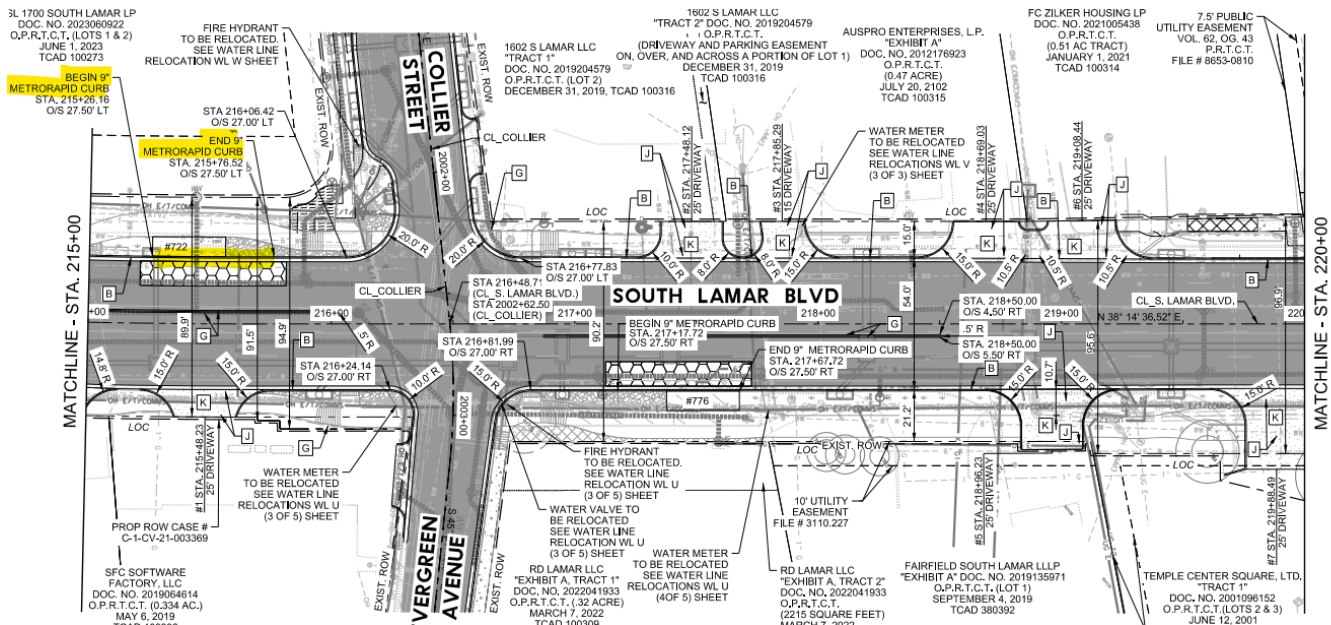

TPW 16: Comment Status:

- Curb ramps must be located so as to provide a continuous accessible path of travel. *Show a curb ramp at S. Lamar and Collier/Evergreen (crossing S. Lamar).*
Reference: TCM, 4.2.3




TPW 17: Comment Status:

- Driveways must be separated from adjacent driveways by at least 200 feet (S. Lamar).
Reference: TCM, Table 7-5


- On Level 3 or higher roadways, left turns exiting driveways are prohibited without a signal or protected operation.
Reference: TCM, 7.3.0
- A waiver may be requested and will be approved if the driveway is right-in, right-out only and adheres to the standard detail (shown below). <https://atd.knack.com/development-services#customer-portal/services/tpw-waiver/>. Please note a waiver review fee will be assessed.
- Note the direction of flow on the site plan and show locations of "one-way" and "do not enter" signs.
Reference: TCM, 9.3.4.2.H and Fig. 9-12

RIGHT-IN / RIGHT-OUT ISLANDS AT DRIVEWAYS

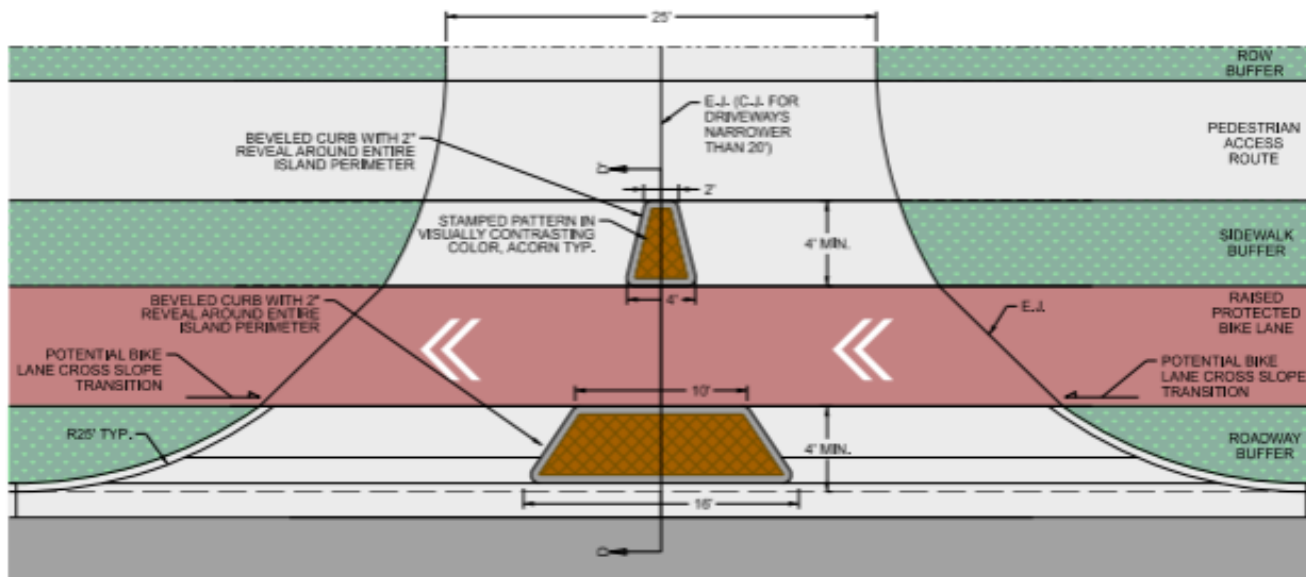

SECTION D-D'

SEE SHEET 9 FOR WIDTH AND GRADING DETAILS

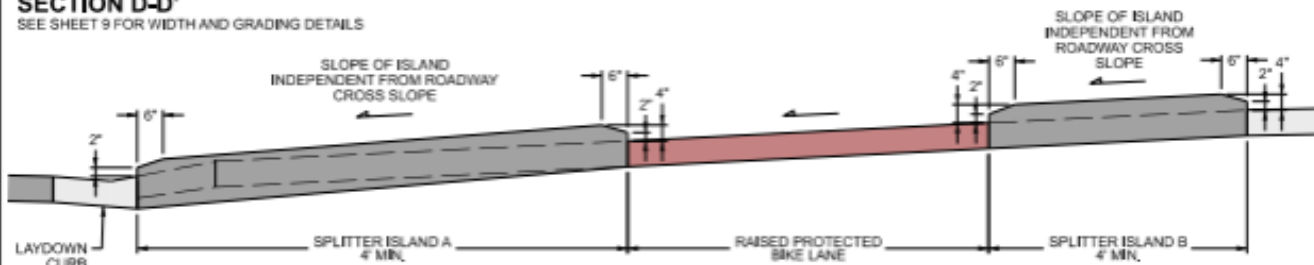

TPW 18: Comment Status:

- If left turning paths into driveways on opposing sides of a street cross each other (offset left), access shall be restricted to right-in, right-out, with the exception of a hooded left-turn into one driveway.
Applicable to Collier Street driveway. A waiver may be requested. <https://atd.knack.com/development-services#customer-portal/services/tpw-waiver/>.
Reference: TCM, 7.6.3.A

TPW 19: Comment Status:

- Trash dumpsters must be located to provide adequate access and maneuverability for service vehicles. *Please verify turning movements for trash collection can be entirely on-site.*
Reference: LDC 25-2-1067(c); TCM, 9.4.1.C

TPW 20: Comment Status:

- All long-term bicycle parking should be covered to provide weather-protected parking. Depict and *dimension the long-term bike parking area on the site plan. Provide details of the rack to be used.*
Reference: TCM, 9.8.3.D.

Addressing Review – Brystin Herbeck (512) 974-7709 -
brystin.herbeck@austintexas.gov

AD1 – Current Status: Cleared

- U0: ~~Please do not use the address number 1700 South Lamar as part of the project name. For example, use 'Main St Commons' instead of '1515 Main Street Commons'. Please update the project name prior to your resubmittal to prevent rejection from the Address Management Team. Project name has been updated to reflect Lamar + Collier~~

AD2 – Current Status: Pending

- U0: To confirm the units are in appropriate order based on our standards, reach out to your reviewer to set up a meeting to discuss the layout. If we find that units are not following our standards during formal review, we will ask you to revise them prior to submitting for Commercial plan review.

If you cannot submit a unit layout during formal review, keep in mind it must undergo an Addressing Review prior to the Commercial or Residential Plan Review submittal. To ensure that the units are in the system and ready for permitting, please submit an Address Review request to Addressing@austintexas.gov and include a PDF attachment of the layout. Indicate "Addressing SP-2026-0136C Unit Review for 1700 South Lamar" in the subject line. Please note that any changes to the units will require a new Addressing Review. You can refer to the Addressing Standards for instructions on how to address units within a multi-story building using the reference link below.

[911AddressingStandards.pdf](#)

Drainage Engineering Review – Connor Flanagan, P.E.
connor.flanagan@austintexas.gov

DE 0 – Current Status: Pending

- U0: Provide a description of any changes made to the drainage design since the last update. If necessary, provide an updated engineering report to reflect those changes.

DE 1 – Current Status: Pending

- U0: If impervious cover is being claimed for existing drainage calculations, please demonstrate that this impervious cover was constructed prior to 1977 or has been permitted prior to this application. The final plat provided on sheet 2 contains a note requiring that runoff *“be held to the amount existing at undeveloped status by ponding or other approved methods.”*

DE 2 – Current Status: Pending

- U0: The plat documents provided on sheet 3 are unofficial copies. Please provide the official documents.

DE 3 – Current Status: Pending

- U0: For the proposed site plan, please provide legal documentation (i.e. approved Land Status Determination) that clearly ties these lots together for the construction, use, and maintenance of the proposed water quality/detention facility. Once received, this reviewer will coordinate with COA Legal staff for review and approval of the legal documents. Any specific questions regarding these documents should be directed towards Annette Bogusch at annette.bogusch@austintexas.gov.

DE 4 – Current Status: Pending

- U0: According to the Engineering Report/summary letter, the zoning for this site only allows up to 80% impervious cover, but the Appendix Q-2 table provided on sheet 12 states that 95% impervious cover is allowed. Please rectify this discrepancy.

APPENDIX Q-2 IMPERVIOUS COVER	
1. IMPERVIOUS COVER ALLOWED AT	<u>95</u> % X (5.21) = 4.95 ACRES

DE 5 – Current Status: Pending

- U0: Provide the fully developed 100-year storm peak flow conditions for the offsite flows. Please note drainage easements are required for the conveyance of offsite flows through the site. The drainage area maps provided on sheets 23-24 list the impervious cover for drainage areas OS-1 and OS-2 as 29% and 24% respectively, which does not represent fully developed conditions. Reference: LDC 25-7-151 & 25-7-152

DE 6 – Current Status: Pending


- U0: Based on the analysis point summary table provided on sheet 24, runoff is increasing from the site at multiple points of analysis for several storm events. Stormwater runoff peak flow rates shall not be increased at any point of discharge from a site for the two (2), ten (10), 25 and 100-year storm frequency events. Please provide the information necessary to verify compliance. If proposed conditions result in increased runoff, the flow must be detained to existing conditions or the site must participate in RSMP.

Reference: DCM 1.2.2(D)

ANALYSIS POINT COMPARISON				
STORM CONDITIONS		ANALYSIS POINT 1	ANALYSIS POINT 2	ANALYSIS POINT 3
2-YR	PRE-DEVELOPMENT	11.30	10.41	3.48
	POST-DEVELOPMENT	11.87	3.93	3.07
10-YR	PRE-DEVELOPMENT	23.33	23.50	7.07
	POST-DEVELOPMENT	19.22	9.92	7.76
25-YR	PRE-DEVELOPMENT	29.19	29.80	8.83
	POST-DEVELOPMENT	22.42	12.84	10.03
100-YR	PRE-DEVELOPMENT	38.71	39.90	11.68
	POST-DEVELOPMENT	27.19	17.53	13.71

DE 7 – Current Status: Pending

- U0: Based on the proposed drainage area map provided on sheet 24, the location of Analysis Point 2 does match the actual point of discharge from the site.

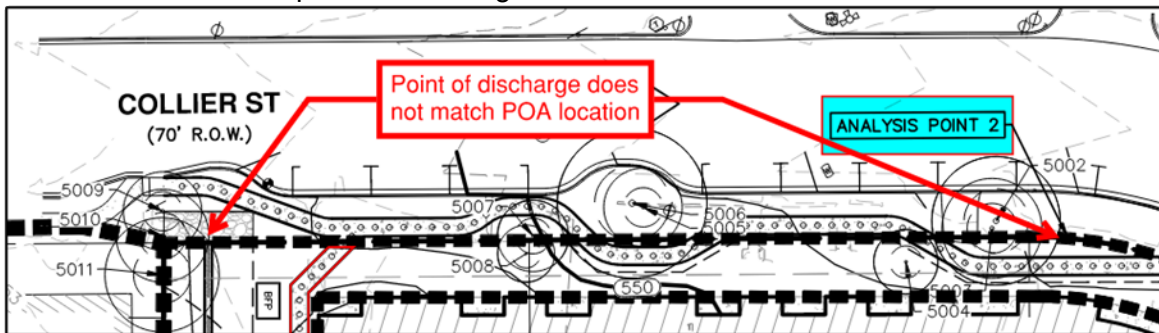

DE 8 – Current Status: Pending

- U0: Demonstrate adequate conveyance of off-site runoff through the site. The proposed “trickle channel” conveying offsite flows from the drainage area OS-1 is considered an open public channel and therefore must comply with requirements outlined in DCM Section 6. A drainage easement is also required to contain the channel. Easements will be submitted to legal for review once design related comments are cleared.

Reference: LDC 25-7-151; LDC 25-7-152

DE 9 – Current Status: Pending

- U0: Provide plan/profile sheets for all channels in ROW or public drainage easements to demonstrate compliance with DCM Section 6. Profiles should clearly identify:
 - 25- and 100-year depths of flows, velocities, flowrates for each segment of the channel
 - 25- and 100-year HGLs
 - Beginning and end of construction stations (proceeding from downstream to upstream)
 - Beginning and end stations for permanent erosion control material, if used

DE 10 – Current Status: Pending

- U0: Provide cross sections for all segments of all channels in ROW or public drainage easements. Cross sections should clearly identify the following:
 - Bottom width
 - Side slopes
 - Concrete pilot channel (if used)
 - Height of channel lining (if used)

- Maximum and minimum depth of channel
- Manning's "n" values

Reference: DCM Section 6; DCM Table 6-2

DE 11 – Current Status: Pending

- U0: Clearly show and label all existing and proposed drainage easements on the drainage layout sheet and all drainage related sheets as per final plat or by separate instrument.

DE 12 – Current Status: Pending

- U0: All proposed drainage easements must meet the minimum easement width requirements. Easements will be submitted to legal for review once design related comments are cleared.
Reference: DCM 1.2.4(G)

DE 13 – Current Status: Pending

- U0: The inlet summary table provided on sheet 26 lists drainage areas that are not shown or labeled in the storm drain plan on sheet 25 (i.e. SD-4A, SD-4B, etc.). Please clarify the location and delineation of these drainage areas.

DE 14 – Current Status: Pending

- U0: Provide an inlet drainage area map and calculations to demonstrate adequate sizing of public inlets. For inlets in public drainage easements or ROW, provide an Inlet Flow Calculation table as described in the Drainage Criteria Manual.
Reference: DCM 4.4.3

DE 15 – Current Status: Pending

- U0: The use of grate inlets, combination inlets, slotted drains, and trench drains in a public drainage easement or ROW must be approved by the Watershed Protection Department.
Reference: DCM 4.1.0(G); DCM 4.1.0(H)

DE 16 – Current Status: Pending

- U0: All public storm lines located in public easements must be centered within the easement.

DE 17 – Current Status: Pending

- U0: All proposed storm drains that will be in the ROW or in a public drainage easement must meet DCM Section 5 design guidelines. The material and diameter of all public storm drains should be a minimum of 18" RCP and should be noted on the drainage plan sheet.
Reference: DCM 5.2.0(J); DCM 5.3.3

DE 18 – Current Status: Pending

- U0: Provide the 25- and 100-year depths of flows, velocities, flowrates and HGLs on all public pipe plan and profile(s).

DE 19 – Current Status: Pending

- U0: Demonstrate adequate depth of cover and clearance for proposed storm drains.
Reference: DCM 5.7.0

DE 20 – Current Status: Pending


- U0: Show all utility crossings of the public storm drains in the profiles. Demonstrate adequate vertical clearance at all crossings.
Reference: DCM 5.7.0

DE 21 – Current Status: Pending

- U0: Demonstrate adequate horizontal clearance between the public storm drains and other utilities. Call out any areas where minimum clearances are not being met.
Reference: DCM 5.7.0


DE 22 – Current Status: Pending

- U0: Please provide more information in the plans to clarify the proposed configuration of the connection into the existing storm system within South Lamar Boulevard. The proposed wye in this location does not appear to be code compliant.

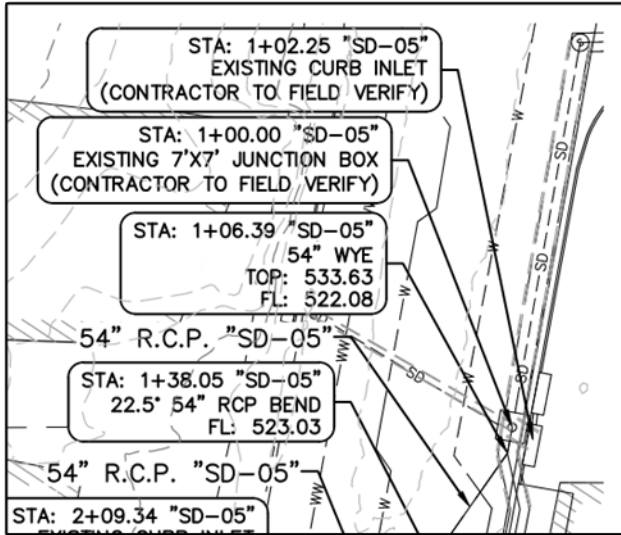

DE 23 – Current Status: Pending

- U0: Please clean up and layer control the storm drain layout sheets, specifically the plan view for SD-04 and SD-05 on sheet 28. The current plants are congested, difficult to interpret, and the location of the proposed storm lines are not visible/legible in the plan view. Engineer of record is encouraged to thoroughly QA/QC plans prior to resubmittal.

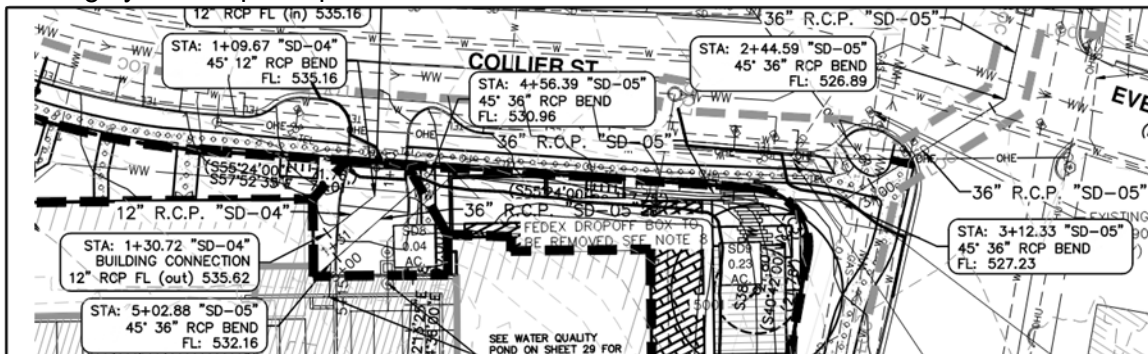

DE 24 – Current Status: Pending

- U0: A development must spread all concentrated discharge to sheet flow before stormwater leaves the property or flows onto the street or sidewalk area from stormwater management facilities or other improvements. If the concentrated discharge cannot be spread to sheet flow levels, the development shall be required to connect to an existing storm drainage system.
Reference: DCM 1.2.3(D)(2)

DE 25 – Current Status: Pending

- U0: Concentrated discharge across a sidewalk area will not be allowed. Stormwater can be spread under the sidewalk area using a channel section or other method if:
 - the outlet device utilizes sheet flow methods,
 - maintains a minimum three (3) foot horizontal separation from all utility infrastructure, and
 - is approved by the Transportation and Public Works Department.

Reference: DCM 1.2.3(D)(3)

DE 26 – Current Status: Pending

- U0: The profile view provided on sheet 27 labeled “SD-01” appears to be for the conveyance “trickle channel”, but it shows a 12” R.C.P. pipe located above both existing and proposed grade.

DE 27 – Current Status: Pending

- U0: Every point within the storm drain must be a maximum of 250 feet from an access point for storm drains 30 inches in diameter or smaller. For storm drains greater than 30 inches in diameter, manholes shall be placed so that there is a maximum distance of 300 feet to an access point. Inlets and storm drain outfalls may be considered as access points for maintenance purposes. Access points must be accessible in accordance with the maintenance and construction requirements outlined in the DCM. Please demonstrate compliance.

Reference: DCM 5.6.1; DCM 1.2.4(E)

DE 28 – Current Status: Pending

- U0: Public storm lines must not contain more than one horizontal bend between access points, with that bend having a deflection of no more than forty-five (45) degrees in the direction of flow, and no vertical bend with a deflection of greater than five (5) degrees.

Reference: DCM 5.6.1


DE 29 – Current Status: Pending

- U0: A public manhole shall be placed at the transition point of a storm drain from private to public.

Reference: DCM 5.6.2

DE 30 – Current Status: Pending


- U0: A manhole shall be placed at locations where changes in pipe size occur. Please demonstrate compliance.

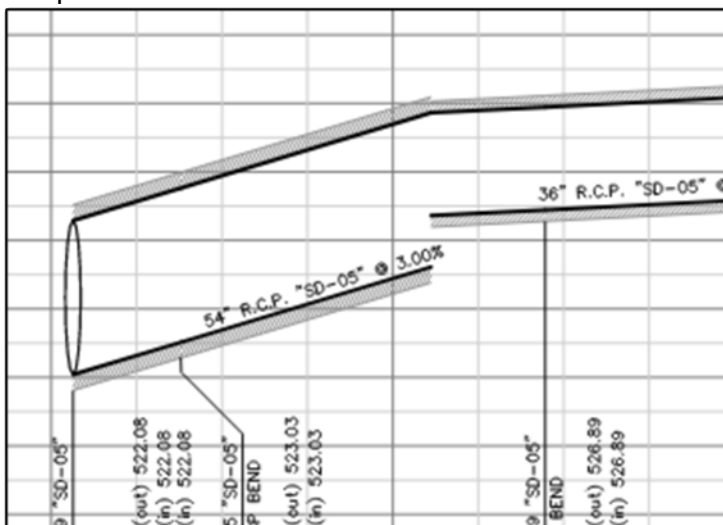

Reference: DCM 5.6.0

DE 31 – Current Status: Pending

- U0: There appears to be multiple instances of redundant call outs and viewport cutoffs throughout the plans which make it difficult to interpret the intended design. Engineer of record is encouraged to thoroughly QA/QC plans prior to resubmittal.

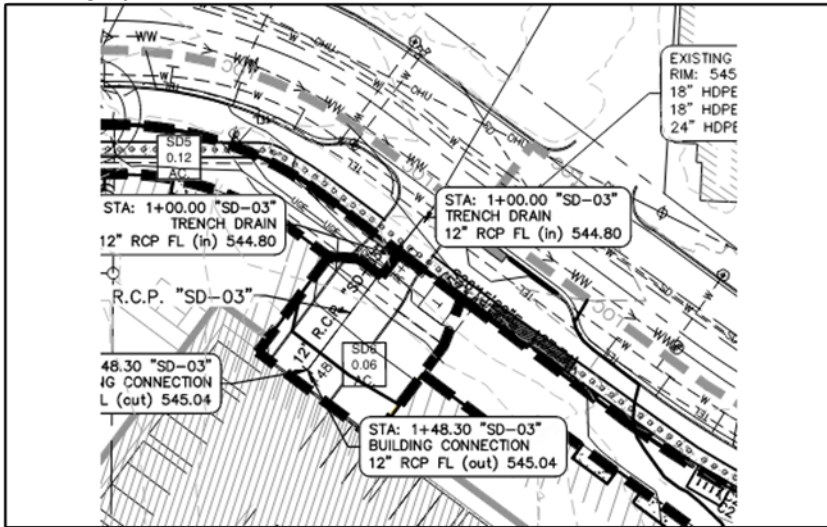

DE 32 – Current Status: Pending

- U0: Please provide more information about the intended purpose of storm line SD-03 shown on sheet 28. The plans appear to show that both the surface grading and the underground building connection line are sloped towards the proposed trench drain without any connection to discharge the flow, so there is nowhere for the collected runoff to go.

DE 33 – Current Status: Pending

- U0: Demonstrate compliance with all applicable maintenance and construction requirements outlined in the Drainage Criteria Manual.
Reference: DCM 1.2.4(E)

DE 34 – Current Status: Pending

- U0: Submit a signed and sealed engineering report for the detention pond with each update. The plan set sheets included in the engineer's report will need to be updated to reflect any changes prior to final approval. Include the following:
 - Inflow hydrograph for existing and proposed conditions including all runoff factors
 - Pond routing with elevation-discharge and elevation-storage curves
 - Outflow hydrograph

DE 35 – Current Status: Pending

- U0: Please demonstrate the "draw-down" time for the proposed detention pond will not exceed 24-hours from the time of peak storage to the time of complete emptying of the pond, as determined by hydrograph routing or other calculations acceptable to the City.
Reference: DCM 8.3.2(C)

DE 36 – Current Status: Pending

- U0: Provide a Subsurface Pond Maintenance Plan and a SPM Restrictive Covenant. The site plan will not be approved until the SPM RC document number is provided on the cover sheet of the plans.

6/1/26

Update #0

Environmental Review – Kymberli Herron (512) 921-1410 -
kymberli.herron@austintexas.gov

COVER SHEET NOTES

EV 01 – U0: Add a note to the cover sheet stating: “This project is located in the West Bouldin Creek Watershed, which is classified as an Urban Watershed.”

EV 02 – U0: Add a note to the cover sheet stating: “This site is not located over the Edwards Aquifer Recharge Zone.”

IMPERVIOUS COVER

EV 03 – U0: Remove the Q1 and Q2 tables. These are not applicable in Urban watersheds. [LDC 25-8-372]

ESC REQUIREMENTS [LDC 25-7-61,65, 25-8-181,182,183,184]

EV 04 – U0: Add the following notes to all ESC sheets:

If disturbed area is not to be worked for more than 14 days, disturbed area needs to be stabilized by revegetation, mulch, tarp, or revegetation matting. [ECM 1.4.4.B.3, Section 5.]

Environmental Inspector has the authority to add and/or modify erosion/sedimentation controls on site to keep project in compliance with the City of Austin Rules and Regulations [LDC 25-8-182]

Contractor shall utilize dust control measures during site construction such as irrigation trucks and mulching as per ECM 1.4.5(A), or as directed by the Environmental Inspector.

The contractor will clean up spoils that migrate onto the roads a minimum of once daily. [ECM 1.4.4.D.4]

Per LDC 25-8-323(C), for areas on the site that are to remain pervious after development, any soils that are compacted during site grading and construction operations must be decompacted in compliance with the ECM and in compliance with SSM 661S.

All disturbed areas to be revegetated are required to have a minimum of six (6) inches of topsoil. Topsoil shall meet the definition in Standard Specification 601S.3. In areas where no topsoil exists, or where topsoil is needed for vegetative establishment, the subgrade shall be loosened by discing or scarifying to a depth of at least two (2) inches prior to placement of six (6) inches of topsoil. [ECM 1.4.7, Appendix P-1]

Permanent vegetative stabilization of areas disturbed by construction shall be per ECM Appendix P-1, unless otherwise indicated on the plan.

SEDIMENT CAPTURE

EV 05 – U0: **Address the following on the ESC Plan and Pond Related Sheets:**

- The sheet index claims a pond; the pond sheet shows no pond. Per the ECM the quantity of silt fence required is greater if there is no water quality pond is on site to act as a temporary sediment basin

during construction activities. Specify in the comment response letter if a water quality detention pond is proposed and update the plan set as necessary. Additional ESC review and comment are pending per ECM Section 1.

- If a Pond is proposed, apply the following as applicable Per ECM 1.6.7.5.H, the following apply to rain garden vegetation. Per ECM 1.6.7.5.C, the following apply to biofiltration vegetation.
- Surface water should be prevented from entering into the LOC from offsite upslope areas. Provided that it won't flood other property, add silt fence along the entire upslope LOC boundary to prevent surface water from draining into the LOC. [ECM 1.4.4.B.2]
- Designate a staging area and temporary spoils area and provide a row of silt fence located immediately downslope of the spoils area. [ECM 1.4.4.B.3] This area is notated but not clearly shown on the ESC plan sheet.
- Provide a single, overall ESC sheet. Additional comments pending.
- Please ensure the silt fencing label is clearly identifiable.

DETAILS

EV 06 – U0: Add the following detail(s) to the plan set:

- Concrete washout
 - Mulch log detail ECM Figure 1.4.5.F
 - J-hook detail ECM Figure 1.4.5.G.4
 - Silt fence turnback detail ECM Figure 1.4.5.G.3
 - Dewatering skimmer detail ECM Figure 1.4.5.K.1., pending confirmation of pond
 - Curb & Gutter Section (430S-1)
- [LDC 25-8-181, LDC 25-8-604, ECM 3.5.2, ECM 1.4.1.1(C)]

LANDSCAPE

EV 07 – U0: Provide a Landscape Plan that is compliant with Chapter 25-2, Subchapter C, Article 9 of the City of Austin Land Development Code, and Section 2 of the City of Austin Environmental Criteria Manual. Further landscape and tree replacement review and comments may be pending. Please ensure cover sheet plan index match page numbers to reference material correctly.

EV 08 – U0: Add the following notes to the landscape plan:

The Owner will continuously maintain the required landscaping in accordance with LDC 25-2-984.

Supplemental irrigation is required for newly planted, required landscape plants per LDC 25-8-1008, ECM 2.4.6, and ECM appendix O.

EV 09 – U0: Add planting detail ECM Figure 3-14 to the landscape plans.

PLAN GRAPHICS

EV 10 – U0: Show on the plan specific location, species, container size, and quantities of new shrubs, ground covers and grasses. [ECM 2.4]

EV 11 – U0: Show on the plan specific location, species, size and quantities of new trees. New trees to be planted shall be at least six feet in height and 1 1/2 caliper inches. Label each tree to indicate which of the following requirements it satisfies:

- Street yard trees
- Replacement trees

- Parking lot trees
 - Buffer trees
- [ECM 2.4.1(D)]

STREET YARD

EV 12 – U0: Street yard trees must be provided in accordance with ECM 2.4.1.D.

EV 13 – U0: Show and label the graphic delineation of the street yard area on the landscape plan. [LDC Section 25-2-1003, ECM 2.4.1]

EV 14 – U0: Twenty percent of the street yard must be landscaped. Demonstrate compliance with this requirement. [ECM 2.4.1]

EV 15 – U0: The proposed commercial / MF project must be screened from adjacent residential properties with a solid wood or masonry fence or with vegetation in compliance with ECM 2.9.1.B or C. [LDC 25-2-1006; ECM 2.9.1]

FEES AND ESC FISCAL SURETY [LDC 25-1-82, 25-7-65, 25-8-234]

EV 16 – U0: Payment of the site plan environmental inspection fee is required prior to permit/site plan approval. The fee is payable through the AB+C portal. EV Review will be approved prior to payment of this fee. However, the applicant is advised that the permit issuance will not occur until this fee has been paid. **The case manager will confirm payment of the environmental inspection fee prior to permit issuance.**

EV 17 – U0: Payment of the landscape inspection fee is required prior to permit/site plan approval. The fee is payable through the AB+C portal. EV Review will be approved prior to payment of this fee. However, the applicant is advised that the permit issuance will not occur until this fee has been paid. **The case manager will confirm payment of the landscape inspection fee prior to permit issuance.**

EV 18 – U0: Provide a fiscal estimate for erosion/sedimentation controls and revegetation based on ECM Appendix S-1. For sites with a limit of construction greater than one acre, the fiscal estimate must include a \$3000 per acre of LOC clean-up fee. The approved amount must be posted with the City prior to permit/site plan approval. [LDC 25-8-186, ECM 1.2.1, ECM Appendix S-1]

Fire For Site Plan Review – Constantino Mendoza (512) 974-2574 -
constantino.mendoza@austintexas.gov

F1 – Current Status: Pending

- **U0:** The width of the fire lane turnaround appears to be less than 25ft. Fire Department access roads must be a minimum of 25 ft wide with a minimum of 14 ft vertical clearance.
Reference: AFD Local Amendment IFC 503.2.1

F2 – Current Status: Pending

- **U0:** Gates across fire access roads must have the appropriate width and electric gates must be provided with a Knox key switch.

Gates for two-way fire access roads should be a minimum of 25ft wide or at least full width of the fire access road.

Gates for one way fire access roads should be a minimum of 15ft wide.

***Provide the following notes on all site plans that show gates across fire access roads:

“Provide a Knox Key switch at all power operated gates and a Knox Box at all manual gates across fire access roads for fire department access.”

“All gates across fire access roads shall open the full width of the fire access road so the fire access road is not obstructed in anyway by the gate or any of the gate components.”

“All power operated gates across fire access roads shall be equipped with gate operators listed in accordance with UL 325. Gates intended for automatic operation shall be designed, constructed and installed per ASTM F2200. A manual means of opening the gate in the event of power loss is required.”

Reference: IFC 503.6

F3 – Current Status: Pending

- **U0:** Provide a section view of the proposed median located at the fire lane entrance off S. Lamar Blvd. The section shall be designed per the Transportation Criteria Manual (TCM) and be installed at a height to avoid the equipment under the apparatus.

Reference:

F4 – Current Status: Pending

- **U0:** Adequate fire flow must be available for the worst-case building on the Site Plan. Fire separation is only allowed if the building is separated by fire walls with no openings, constructed per the IBC. The total building fire area shall be used.

Reference: IFC 507.1 & Appendix B

F5 – Current Status: Pending

- **U0:** Fire department connection locations should be shown for sprinkler and standpipe systems. The Fire department connection for standpipe systems should be within 100 ft of a fire hydrant.

Reference: NFPA 14 Section 6.4.5.4. and IFC Section 507.5.1.1.

F6 – Current Status: Pending

- **U0:** The Southwest portion of the building appears to not have a second hydrant covering this area. AFD requires a minimum of 1 hydrant within 400 ft of all portions of exterior walls. A second hydrant is required within 500 ft if the fire flow is 1500 gpm or more.

Reference: IFC 507.5.1

F7 – Current Status: Pending

- **U0:** The building appears to meet the definition of a high rise per the IFC/IBC. A building is classified as a high rise when the highest occupied floor is more than 75ft above the lowest level of fire department access. Due to this building utilizing Collier Street and South Lamar Boulevard, the lowest level shall be measured from either street.


Reference: IFC chapter 2

LDE1: The 10' wide curb inlet located on Collier Street shown on the Utility Plan must be a minimum of 10' away from the end of the proposed driveway radius.

Industrial Waste Review – Jonathan Bode (512) 972-1086 -
jonathan.bode@austintexas.gov

Update #0
Rejected

- **U0: If WW lateral = $8'' \leq \phi \leq 12''$:**
For compliance with §15-10-226 of the Austin City Code and UCM 2.9.4.G.5, install a City of Austin approved **large diameter cleanout** per Standard Detail 506-AW-04 to act as a sampling and inspection port. Reference the detail in the call-out and include the detail in the utility detail sheets. Per UCM 2.9.4.G.7, the cleanout must be located at or near the property line within the public right-of-way (ROW) or utility easement line. The cleanout **shall not** be located in a vehicle traffic area, parking area, load bearing pavement, sidewalk, or driveway. Be aware there is a 14' foot depth limit for the large diameter cleanout structure.

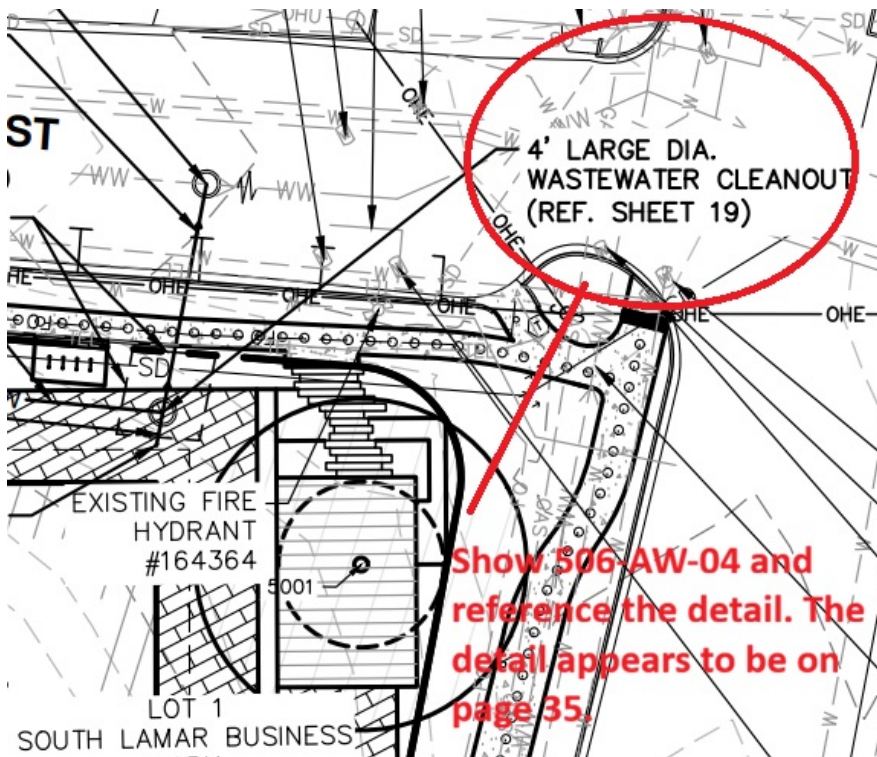

PARD / Planning & Design Review – Kathleen Stanford (512) 974-9717 -
kathleen.stanford@austintexas.gov

Update 0 – 6/3/2026:

PR1 – Current Status: Pending.

- U0: Please reach out to this reviewer (Kathleen.Stanford@austintexas.gov) to schedule a meeting to discuss parkland dedication requirements for this development.

PR2 – Current Status: FYI.

- U0: A Parkland Early Determination (PED #2178) was issued on 04/28/2026 stating that land dedication would be owed for this project due to the opportunity for on-site parkland to address park deficiency in the area.

PR3 – Current Status: Pending.

- U0: Parkland Dedication is required by City Code prior to approval of this site plan. If the amount of land provided does not equal the amount required by City Code §25-1-603 (C), additional fees in-lieu of land may be required. Please confirm the total residential unit count, including market-rate and certified affordable units, if any. The site plan currently shows 459 market-rate units.
Reference: LDC §25-1-603, §25-1-603 (C)

PR4 – Current Status: Pending.

- U0: For multifamily developments, parkland dedication may not exceed 10 percent of the gross site area. Please confirm the gross site area for your project. The site plan currently lists/shows 5.21 acres.
Reference: LDC §25-1-603, §25-1-603 (D)

PR5 – Current Status: Pending.

- U0: Parkland will be required along Collier St on the northwest side of the development, with approximately 150 to 200 LF of ROW frontage and sufficient depth to accommodate passive and active recreational amenities. The fire lane and 75 ft setback should be excluded from the proposed parkland. Please refer to the screen capture below. Parkland configuration and planning to be discussed with the applicant. This comment will be cleared once the amount of parkland acreage and configuration are determined.
Reference: BCM §14.3.7

Parkland dedication has been provided for [#] units by the recordation of a /deed conveying [#] acres. The remaining fee-in-lieu of parkland dedication must be paid prior to the issuance of a certificate of occupancy. No certificate of occupancy may be issued for this development until receipt of payment. Contact the Austin Parks and Recreation prior to requesting inspections.

PR10 – Current Status: FYI.

- U0: Note: Additional comments may be generated based on responses to the above.

Site Plan Review – Randall Rouda (512) 974-3338 - randall.rouda@austintexas.gov

Site Plan Comments Comment Library

SUBDIVISION / LEGAL LOT


SP1 – Current Status: Pending

U0: Site plan review and approval cannot be finalized until the lot(s) is/are legal by recorded plat or grandfathered by Land Status Determination.

Reference 25-1-61

SP2 – Current Status: Pending

- U0: A portion of the tract outside of Lot 1 of the subdivision shown on Sheet 3 is not legal by subdivision; therefore a Land Status Determination is required to determine if it is a legal tract.



In order to make this determination, email Subdivision Review at

DSD_SubdivisionReview@austintexas.gov.

Reference: 25-1-61

SP3 – Current Status: Pending

U0: Show legal description of the property on the cover sheet by lot, block, subdivision, or by metes and bounds. Indicate the book and page or document number with the legal description. To verify legal descriptions and to ensure taxes have been paid, submit Tax Certificates for both parcels comprising Tract 2 of the proposed Site Plan.

SP4 – Current Status: Pending

U0: Show all property boundaries with metes and bounds on the Site Plan Sheet.

SITES WITH MULTIPLE LOTS

SP5 – Current Status: Pending

U0: As proposed, construction such as buildings, drainage and water quality infrastructure, and/or vehicular access and parking facilities are proposed to be constructed across the property line between two separate lots. Please record a Unified Development Agreement (UDA) that clearly ties these lots together for the construction, use, and maintenance of the proposed development. The recorded UDA will be a Restrictive Covenant that may also establish a Joint Use Access Easement and/or a Drainage Easement. Draft UDA templates are available at: <https://www.austintexas.gov/department/forms-applications> . Please submit the applicable document to this reviewer, including Exhibits showing Joint Use Access Easement areas, Drainage Easement Areas and shared Drainage and Water Quality infrastructure. This reviewer will consider the submittal with other affected reviewers and will coordinate with the Legal Department for review and approval. For any legal document questions, please contact Annette Bogusch - DSD Legal Liaison (512) 974-6483. Please be aware that this process takes some time and requires lien-holders information and consent.

SP6 – Current Status: Pending

U0: Note on the cover sheet and site plan sheet: *The site is composed of 4 lots/tracts. It has been approved as one cohesive development. If portions of the lots/tracts are sold, application for subdivision and site plan approval may be required.*

*Once the UDA is recorded, add the document number to the note.

LAND USE / ZONING

SP7 – Current Status: Pending

U0: Clarify the basis for the Density Bonus referenced in the footnote to the Project Tracking Table on the Site Notes and Tables Sheet. Based on conversations with Housing Staff, it is our understanding that the current intent is to rely on the Development Bonus provisions of the DB90 Overlay Zone for the easterly portion of the property and on the provisions of Government Code Chapter 218 (added by SB840) for development on the westerly portion of the property. Where possible, the following comments acknowledge this intent, however, additional comments may be required upon further clarification.

SP8 – Current Status: Pending

U0: Clearly show the zoning boundary (CS-V-CO / CS-V-DB90) on the Site Plan sheet.

SP9 – Current Status: Pending

U0: Provide separate site data tables for the portions of the site and building for the separately zoned portions of the site (Tract 1 and Tract 2) and for the site as a whole. Each site data table should separately show site area, zoning, proposed use(s), number and type of residential units, height, building coverage, impervious cover, gross floor area, and FAR.

Reference 25-2-492

SP10 – Current Status: Pending

U0: Multifamily Residential Development is not permitted in the CS Base Zone. Multifamily Residential development may be permitted with the approval of a DB-90 Development Bonus (on Tract 1), or pursuant to the standards of LGC Chapter 218. Minimum lot area / maximum development density may apply if development is proposed under the standards of LGC Chapter 218.

SP11 – Current Status: Pending

U0: The project exceeds the maximum height (60 feet) in the CS Base Zone on Tract 1. Additional height may be authorized with a DB90 Development Bonus. Correct the 350 foot maximum building height for Tract 2 as shown on Sheet 16 to 60 feet.

SP12 – Current Status: Pending

U0: The project exceeds the maximum FAR of 2:1 in the CS Base Zone. Additional FAR may be authorized with a DB90 Development Bonus or pursuant to the standards of LGC Chapter 218.

SP13 – Current Status: Pending

U0: Maximum Building Coverage in the CS Zone is 95%. Show that maximum in the table on Sheet 16 or clarify which program will be used to override that requirement.

SP14 – Current Status: Pending

U0: Provide a letter from the Housing Department certifying that the project meets the standards of the development bonus program or programs proposed to modify the CS Base Zone standards for land use or development requirements. A letter from the Housing Department is not needed for review of the project pursuant to LGC Chapter 218.

SP15 – Current Status: Pending

U0: Provide exhibits showing the following:

- A) All parcels within 3,000 feet of the property boundary, with sufficient land use, zoning and/or ownership information to confirm that there are no airports (private or public) and no military bases within 3,000 feet of the property boundary.
- B) All parcels within 1,000 feet of the property boundary showing all any hazardous use permits issued by the Austin Fire District. This exhibit should also show whether the site is located within a Clear Zone or Accident Potential Zone.
- C) All parcels within 1,000 feet of the property boundary showing all current Land Uses. Note that the following Heavy Industrial Uses may not be located within 1,000 feet: Basic Industry; General Warehousing and Distribution; Light Manufacturing, Recycling Center, Resource Extraction, or Stockyards.
- D) All parcels within 1,000 feet of the property boundary showing current zoning districts. Note that the Industrial Park (IP), Limited Industrial Service (LI), and Major Industry (MI) Zoning Districts may not be located within 1,000 feet unless a Conditional Overlay (CO) Zone or Planned Development Agreement (PD) restricts the allowed uses on the subject site to remove the Heavy Industrial Uses listed above as allowed uses. If a Planned Unit Development (PUD), Planned Development Agreement (PDA) or Research and Development (R&D) Zoning District or any other stand-land use ordinance is located within 1,000 feet, demonstrate that the most recent enabling ordinance does not include any of the above heavy industrial uses as allowed uses.

SP16 – Current Status: Pending

U0: Demonstrate that the proposed residential density on the portion of the site relying on LGC Chapter 218 is 54 units/acre or less.

SP17 – Current Status: Pending

U0: Specify the elevation (in feet above sea level) of the average of the highest and lowest grades adjacent to the building, and specify the maximum elevation permitted by zoning regulations. The building elevations show the location of the average adjacent grade and maximum height (at 90 feet) but does not provide elevations for those features.

SP18 – Current Status: Pending

U0: Please add the architectural building plan for Level 6.

SP19 – Current Status: Pending

U0: Show or note the type of restaurant (drive-in/fast food, limited or general) and retail (convenience or general) proposed on the site.

SP20 – Current Status: Pending

U0: Please add the following note to the demolition plan exhibit: Demolition subject to Tenant Notification regulations.

Reference 25-1-712

SP21 – Current Status: Pending

U0: Show a 10 foot Street Side Yard Setback along the entire Collier Lane property line.

COMPATIBILITY / SCREENING REQUIREMENTS

SP22 - Current Status: Information only

U0: FYI - The site is subject to compatibility standards due to the adjacency of four SF-3 zoned properties to the west of the subject site (i.e., the triggering property). Note that the adjacent church does not trigger compatibility unless there is at least one residential unit on the site. If the church site does not contain residences, please remove the compatibility buffer lines as measured from that property.

Reference 25-2-1051, 25-2-1053

SP23 - Current Status: Pending

U0: A 25-foot compatibility buffer is required along the property line shared with the triggering property. No vertical structures are permitted in the compatibility buffer. Please label the compatibility buffer on the site plan sheet and/or landscape sheet.

Reference 25-2-1062(B)

SP24 - Current Status: Pending

U0: The compatibility buffer includes a 10-foot screening zone at the triggering property line and a 15-foot restricted use zone that begins at the edge of the screening zone. Please label the screening zone and restricted use zone on the site plan sheet and/or landscape sheet.

Reference 25-8-700

SP25 - Current Status: Pending

U0: Update the Compatibility Notes on Sheet 5 as follows:

- a. All exterior lighting will be hooded or shielded from the view from the site's property line or alleyway that is shared with a triggering property.

- b. The noise level of mechanical equipment will not exceed 70 dba at the property line or alleyway that is shared with a triggering property.
- c. A concrete slab used for a refuse receptacle will be located more than 15 feet from a triggering property.
- d. All on-site amenities, except multi-use trails, are located more than 25 feet from a triggering property.
- e. Vehicle lights, ground floor and rooftop mechanical equipment, outdoor storage, refuse receptacles and collection areas, and common areas for amenities will be screened and will not be visible at the property line or alleyway that is shared with a triggering property.

Reference 25-2-1063

SUBCHAPTER E: DESIGN STANDARDS AND DB-90

SP26 - Current Status: Pending

U0: Please label and dimension the Planting Zone (min. 8' wide), Clear Zone (min. 7' wide), and the Supplemental Zone (if one is proposed) on the Site Plan. See Section 2.2.2.B for design standards.

SP27 - Current Status: Pending

U0: 75% of the net frontage length of the property along the CTC must consist of continuous building façade built up to the clear zone, or the supplemental zone if one is provided. The current proposal does not appear to meet this standard.

Reference: Sub E Sec. 2.2.2.D.1

SP28 - Current Status: Information only

U0: FYI- Utilities must be underground from building to property line. Utilities within the right-of-way must be placed underground or to rear of site to the maximum extent practicable. If overhead utilities remain, no portion of the building may be located within a 10-foot radius of the energized conductor.

Reference: Sub E Sec 2.2.2.B.3

SP29 - Current Status: Pending

U0: If a supplemental zone is provided, up to 30 percent of the linear frontage of the supplemental zone may be a maximum of 30 feet wide, and the remainder of the supplemental zone shall be a maximum of 20 feet wide. It appears that most of the building is located greater than 30 feet from the clear zone.

Reference: Sub E Sec 2.2.2.C

SP30 - Current Status: Pending

U0: At least one customer entrance must face the principal street and connect directly to the sidewalk along the principal street, unless you meet the exception requirements of Section 2.4.B.1. The sidewalk connecting to the principal street from the entrance is required to be shaded. This requirement will be revisited with the building location comments, above.

*Show and label all building entrances and how they connect to the roadway or ICR.

SP31 - Current Status: Pending

U0: Include the following note on the site plan page: "All exterior lighting will be full cut-off and fully shielded in compliance with Subchapter E 2.5 and will be reviewed during building plan review. Any change or substitution of lamp/light fixtures shall be submitted to the Director for approval in accordance with Section 2.5.2.E." Also include Figure 34 from Section 2.5.




Figure 34:
Examples of fully-shielded light fixtures.

SP32 - Current Status: Pending

U0: Verify compliance with screening requirements of Subchapter E Section 2.6.2 by a) Screening from view of person standing on property line on far side of adjacent public street: solid waste collection areas and mechanical equipment and rooftop equipment, not including solar panels (Sec. 2.6.2.A.); b) Incorporate loading docks, truck parking, storage, trash collection/compaction, etc., into building/landscape design. And c) add the following note: *Screening for solid waste collection and loading areas shall be the same as, or of equal quality to, principal building materials.*

SP33 - Current Status: Pending

U0: Coordinate the Site Data Table and Landscape Plan to show a consistent amount of open space to meet Subchapter E Requirements. Show the type of open space proposed and provide dimensions and amenities required for that open space type.
(Example: A landscape area other than one required by Subchapter C, Article 9 (Landscaping), provided such landscaped area has a minimum depth and width of 20 feet and a minimum total area of 650 square feet. The area shall include pedestrian amenities.)

SP34 - Current Status: Pending

U0: The shaded sidewalk shall provide trees planted no more than 30' on center or a 4' awning. Show typical separation for the shade trees along Lamar.

Reference: Sub E Sec 2.8.2.A.3

SP35 - Current Status: Pending

U0: Building entrances and exits, other than those used solely for emergency purposes or for deliveries, shall be located under a shade device such as an awning or portico.

*Show and label all exits and entrances and how each will be shaded.

Reference: Sub E Sec 2.8.2.A.4

SP36 - Current Status: Pending

U0: Demonstrate that both commercial uses on the ground floor meet the following standards:

- a) Provide a customer entrance that opens directly onto the sidewalk.
- b) Minimum depth of not less than 24 feet;
- c) A height of not less than 12 feet, measured from the finished floor to the bottom of the structural members of the ceiling; and
- d) A front façade that meets the glazing requirements of Section 3.2.2. (See Figure 39.)

SP37 - Current Status: Pending

U0: Demonstrate that the following objects are screened sufficiently to not be visible from the westerly property boundary:

- a) ground floor and rooftop mechanical equipment;
- b) outdoor storage;

- c) refuse receptacles and collection areas; or
 - d) common areas for amenities, including outdoor decks, patios, or pools.
- Rooftop mechanical equipment may be screened by a parapet.

DEMOLITIONS AND RELOCATIONS

SP38 - Current Status: Information only


U0: FYI- The applicant is responsible for requesting relocation and demolition permits once the site plan is approved. The City Historic Preservation Officer will review all proposed building demolitions and relocations prior to site plan approval. If a building meets city historic criteria, the Historic Landmark Commission may initiate a historic zoning case on the property. All existing structures shown to be removed will require a demolition permit from the City of Austin Housing and Planning Department. Please contact the Historic Preservation Officer at 512-974-3393 or preservation@austintexas.gov for additional information. Please begin this process as soon as possible as it can take some time.

Reference: Chapter 25-11

ADMINISTRATIVE

SP39 - Current Status: Pending

U0: The proposed structure encroaches over an electrical easement shown on the Amended Plat of Lot 5, Wendlandt's Subdivision and Lot 1 of the Resubdivision of Lots 3 & 4 of Wendlandt's Subdivision. Please refer to <https://www.austintexas.gov/departments/land-development-engineering> and contact landmanagement@austintexas.gov. Provide documentation that the easement have been vacated.



SP40 - Current Status: Pending

U0: Add the following related cases to the cover sheet: Zoning Case No. C14-2024-0163.

SP41 - Current Status: Pending

U0: Confirm that all amenities such as walls, fences, sidewalks, swimming pools, and all other land

improvements are shown on each site plan sheet.

SP42 - Current Status: Pending

U0: Please clearly delineate the footprint of the building including the roofline and any overhangs that may exist.

SP43 - Current Status: Pending

U0: Show the dimensions of all existing and proposed structures.

SP44 - Current Status: Pending

U0: Show the limits of construction (LOC) on the site plan sheet. Include the area necessary for the construction of access drives and all off-site utility work.

SP45 - Current Status: Pending

U0: Show the following site plan release notes on the site plan:


- a. All improvements shall be made in accordance with the released site plan. Any additional improvements will require site plan amendment and approval of the Development Services Department.
- b. Approval of this Site Plan does not include Building and Fire Code approval nor building permit approval.
- c. All signs must comply with requirements of the Land Development Code ([Chapter 25-10](#)).
- d. Additional electric easements may be required at a later date.
- e. Water and wastewater service will be provided by the City of Austin.
- f. All existing structures shown to be removed will require a demolition permit from the City of Austin Development Services Department.
- g. A development permit must be issued prior to an application for a building permit for non-consolidated (A) or Planning Commission approved site plans.
- h. For driveway construction: The owner is responsible for all costs for relocation of, or damage to utilities.
- i. For construction within the right-of-way, a ROW excavation permit is required.

SP46 - Current Status: Pending

U0: Correct the Sheet Numbers and Sheet Index to be complete and consistent.


SP47 - Current Status: Pending

U0: Review the Site Plan Sheets to ensure that all development is identified with callouts or in the Legend. Specifically, identify the features shown below. If the area shown consists of stairs and a raised deck, or similar structure, please include those features on the Elevation Sheets as appropriate.

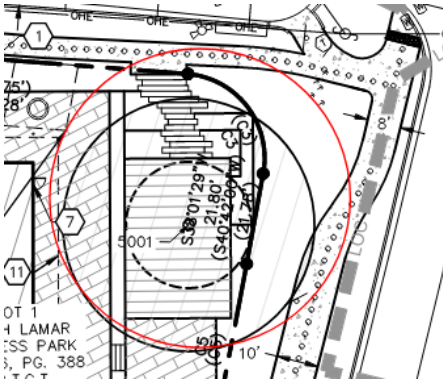

SP48 - Current Status: Pending

U0: Show a development and/or landscape plan for the proposed Courtyard. The plans were not found on the Landscape Sheets as Referenced on the Site Plan Sheet.




SP49 - Current Status: Informational

U0: Note that the prior Site Plan approved on the site: SPC-2011-0259AW; THE MARKET ON COLLIER will be voided upon approval of the proposed Site Plan.

SP50 - Current Status: Pending

U0: Correct the adjacent use to the west of the site from Office to Religious Assembly.

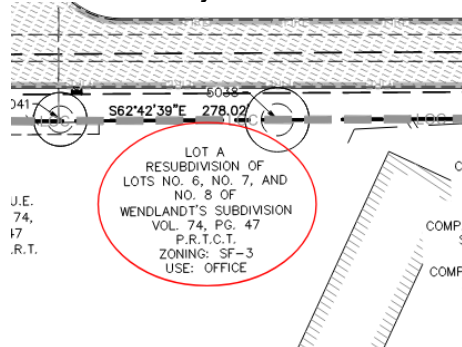

SP51 - Current Status: Pending

U0: Complete or remove the case number in the parking table on Sheet 16.

LOT	TRACT	PROJECT NUMBER	PROJECT NAM
1	1-2	SP-2026-XXXXC	1700 South Lan

Site Plan Plumbing – Cory Harmon (512) 974-2882 - cory.harmon@austintexas.gov

PB1 – Current Status: New comment

- U0: There is private wastewater piping crossing lot lines which is prohibited by Sections 307.1 and 721.1 of the 2024 Uniform Plumbing Code. Revise plans such that the private wastewater piping does not cross lot lines.

PB2 – Current Status: New comment

- U0: On the Overall Utility Plan, Indicate the material of the private domestic water piping.

ATPW Utility Coordination Review – John Carr (512) 974-3212 - john.carr@austintexas.gov

"RW1: Greater than 25 ft of proposed construction on S Lamar Ave, a city-maintained ROW in the full purpose jurisdiction. A Utility Coordination case is required.

Submit AULCC cases online via the Austin Build Connect Portal. Pay the case review fee.

After the fees are paid and your application is processed, you will receive an email invitation with the link and instructions for attending your AULCC meeting date.

AULCC attendees receive the following information specifically regarding their proposed project area:

- Existing utilities
- Proposed utilities
- Current and upcoming activities
- Upcoming special events

Traffic Control Review – Isabell.Pena@austintexas.gov

TPW TCP FYI: Please place deferral note on coversheet to move review out of process and remove traffic control plan from plan set (if present).

TRAFFIC CONTROL PLAN NOTE:

This note is being placed on the plan set in the absence of a temporary traffic control plan (TCP) with the full understanding that if the work cannot be completed using standard and/or special details, then an engineered TCP shall be reviewed and stamped complete by the Right of Way Management Division. Furthermore, a TCP shall be submitted to the [TCP Portal](#) for review a minimum of 6 weeks prior to the start of construction. The applicant/project representative further recognizes that a TCP review fee is required for the initial review and all re-reviews, as prescribed by the most current version of the City's fee ordinance.

The following must be taken into consideration:

- Refer to the "Mobility Guidelines" for developing traffic control strategies <http://www.austintexas.gov/page/mobility-guidelines>
- A traffic control plan is not a permit

AW Utility Development Services – Bradley Barron bradley.barron@austintexas.gov

AW1. – Current Status: Pending from Completeness Check & Not Addressed

U0: For Standard drawings in portrait orientation, a maximum of 8 detail pages per sheet shall be provided and adjusted for size to utilize the entire sheet. For Standard drawings in landscape orientation, drawings shall be provided on a dedicated plan sheet and adjust for size to utilize the entire sheet. All AW details shall be on dedicated AW detail sheets (not interspersed with details from other departments). All Standard drawings shall be legible and obtained directly from COA's Municode site.

Reference: Reference: Per Utility Criteria Manual 2.5.1(E)(20)

AW2. – Current Status: Pending from Completeness Check & Not Addressed

U0: For all lots within proposed development, provide copy of recorded final plat or land status determination letter/report; or, with Pipeline Engineering approval, an approved final plat case (awaiting recording). This must be included as a sheet in the plan set.

Reference: Per Utility Criteria Manual 2.5.1(E)(13) and §25-1-61

AW3. – Current Status: Pending

U0: Service Extension Requests 6368 (W) and 6369 (WW) are currently in review and must be approved prior to development plan approval. For status, contact Christine Perez at (512)972-0035 or Christine.Perez@austintexas.gov.

Reference: Per §25-9

AW4. – Current Status: Pending

U0: The landowner intends to serve the site with City of Austin water and wastewater utilities. The landowner, at own expense, will be responsible for providing any water and wastewater utility improvements, offsite main extensions, utility relocations and or abandonments required. The water and wastewater utility plan must be reviewed and approved by Austin Water for compliance with City criteria. All water and wastewater construction must be inspected by the City of Austin. The landowner must pay the City inspection fee with the utility construction. The landowner must pay the tap and impact fee once the landowner makes an application for a City of Austin water and wastewater utility tap permit.

Reference: Per Utility Criteria Manual Section 2, §15-9, §25-4, §25-5, §25-9, and the Uniform Plumbing Code

FYI: For plan review status contact your assigned Pipeline Engineering reviewer.

Water Quality Review – Connor Flanagan, P.E. connor.flanagan@austintexas.gov

WQ 0 – Current Status: Pending

- U0: Provide a description of any changes made to the water quality design since the last update. If necessary, provide an updated engineering report to reflect those changes.

WQ 1 – Current Status: Pending

- U0: Projects submitted after November 7, 2022, will be required to provide green stormwater control measures. Administrative waivers may be granted on a case-by-case basis but are not guaranteed. The ordinance document can be found here (see pg. 24-26 for green infrastructure requirements): <https://services.austintexas.gov/edims/document.cfm?id=399108>

Reference: Ordinance No. 20221027-045, Part 18; LDC 25-8-213 (C) & (D); ECM 1.6.7

WQ 2 – Current Status: Pending

- U0: The grading and drainage plans should clearly demonstrate how runoff from all proposed on-site development is being routed to the water quality pond for treatment. Based on the proposed drainage area map provided on sheet 24, there appears to be roughly 1,000SF of proposed sidewalk in drainage area PR-2 that is not being captured and conveyed to the water quality pond. It also appears that the entire southern drive aisle in PR-1 and various other proposed sidewalk areas around the site are not being captured and routed to the water quality pond for treatment.

Reference: LDC 25-8-211

WQ 3 – Current Status: Pending

- U0: For the subsurface water quality pond, the access hatches must be centrally located within each basin and must be at least 5 feet from each wall. Access requirements also apply to the subsurface detention basin and a minimum of at least one 4'x6' access hatch is required.

Reference: Figure 1.6.2.E – Subsurface SCM Minimum Design Standards

WQ 4 – Current Status: Pending

- U0: Provide inlet velocity calculations to demonstrate that the maximum velocity entering the water quality basin is two (2) feet per second.

Reference: ECM 1.6.2.B.1.c.

WQ 5 – Current Status: Pending

- U0: Please provide Certification of Compliance – Applications Related to a Closed Municipal Solid Waste Landfill. The certification form can be found at the following website:

WQ 6 – Current Status: Pending

- U0: It appears that base impervious is being claimed. Please provide the base, redeveloped and new impervious cover square footage. Clearly identify these areas separately in the site plan with appropriate shading and labeling for each category of impervious cover. This information is necessary to verify that the water quality pond is providing the required level of treatment.

Reference: ECM 1.9.2

WQ 7 – Current Status: Pending

- U0: Demonstrate compliance with all applicable drainage facilities design and maintenance requirements.

Reference: DCM 1.2.4.(E)

WQ 8 – Current Status: Pending

- U0: For filtration pond types (with underdrains), demonstrate compliance with all underdrain piping and cleanout requirements. All cleanouts should be flush with the top of the media bed or the proposed grade. Cleanouts must be provided at all bends and connections. Additionally, there should be a cleanout placed at least every 50-feet along the underdrain lines. Any lines with more than 50-feet between cleanouts will need to add intermediate cleanout(s) in-between.

Reference: ECM 1.6.5(A)(4)

WQ 9 – Current Status: Pending

- U0: Reduce the gabion wall to less than six (6) feet in height. If site-specific constraints prevent lowering the gabion wall to below six feet, the City may allow a taller wall with additional structural support to ensure its stability.

Reference: ECM 1.6.5(B)(2).

WQ 10 – Current Status: Pending

- U0: Provide a gabion wall detail that meets ECM requirements. The detail should indicate that the Gabion Wall shall be constructed in accordance with City of Austin Standard Specification 594S. The Standard Specifications are online at:

https://library.municode.com/tx/austin/codes/standard_specifications_manual?nodeId=AUSTIN_TX_STANDARD_SPECIFICATIONS_TECHNICAL_MANUAL_SERIES_500PIAP_ITEM_NO_594SGARE_MA9-26-12.

Reference: ECM 1.6.5(B)(2) (“Outlet Structure”)

WQ 11 – Current Status: Pending

- U0: Provide plans, details, and notes for the proposed pump(s) and wet well(s).

Reference: ECM 1.6.7.5(A)(3)

WQ 12 – Current Status: Pending

- U0: Please place the following notes on the pond sheet:
 - *A dual pump system is required with each pump capable of delivering 100% of the design capacity.*

- *Plug valves must be located outside the wet well on the discharge side of each pump to isolate pumps for maintenance and throttling. Please include the required plug valves in the design.*
- *Four control settings must be used: one for starting the pump, one for shutting off the pump at the normal low water level, one for back up shut off the pump in case the first shut-off fails, and one to indicate a high-water level. 4900*
- *An alarm system shall be provided consisting of a red light located at a height of at least 5 feet above the ground level at the wet well. The alarm shall be activated when:*
 - o *The high-water level has been maintained in excess of 72 hours.*
 - o *The water level is below the shutoff float and the pump has not turned off.*
 - o *The high/low-pressure pump shut off switch has been activated.*
- *The alarm must be vandal proof and weather resistant.*
- *A green "pump run light" shall be provided which is activated any time a pump is running. The green light should be located directly adjacent to the red alarm light. Provide pump details indicating this.*
- *All irrigation system distribution and lateral piping (i.e., from the pumps to the spray heads) must be Schedule 80 PVC. All pipes and electrical bundles passing beneath driveways or paved areas must be sleeved with PVC Class 200 pipe with solvent welded joints. Sleeve diameter must equal twice that of the pipe or electrical bundle.*
- *All valves must be designed specifically for sediment bearing water and be of appropriate design for the intended purpose. All remote control, gate, and quick coupling valves must be located in ten-inch or larger plastic valve boxes. All pipes and valves must be marked to indicate that they contain non-potable water. All piping must be buried to protect it from weather and vandalism. The depth and method of burial must be adequate to protect the pipe from vehicular traffic such as maintenance equipment. Velocities in all pipelines should be sufficient to prevent settling of solids. The irrigation design and layout must be integrated with the tree protection plan and presented as part of the Site Plan or Subdivision Construction Plan.*
- *Systems must include a plug valve to allow flushing at the end of every line.*

Reference: ECM 1.6.7.5(A)(3)

WQ 13 – Current Status: Pending

- U0: Place a sign on or near the control box with the name and phone number of the operator of the pump system in case of emergency or maintenance concerns.

WQ 14 – Current Status: Pending

- U0: A separate wet well outside of the basin must be provided for the pumps. The wet well must be constructed of precast or cast in place concrete. Additionally, buoyancy calculations must be provided to demonstrate the wet well will not float under soil-saturated conditions.

WQ 15 – Current Status: Pending

- U0: Please place the following note on the cover sheet: "For Maintenance of the Water Quality and/or Detention facility, see agreement filed in document No. _____, Official Public Records, Travis County, Texas."

AW Pipeline Engineering – David Lara (512) 972-0042 - david.lara2@austintexas.gov
--

AWPE U0 REDLINED CAN BE FOUND HERE: [https://studio.bluebeam.com/share/\\$UmJYSEphZjhuR0p](https://studio.bluebeam.com/share/$UmJYSEphZjhuR0p)

THIS PROJECT WILL NEED TO BE RESUBMITTED FOR ANOTHER PIPELINE ENGINEERING REVIEW. THE MAJOR REASONS FOR ADDITIONAL REVIEW MAY INCLUDE, BUT ARE NOT LIMITED TO NON-COMPLIANCE WITH THE FOLLOWING CITY CODE SECTIONS:

- **§ 30-2-191 – Water Lines (Austin/Travis County Subdivision)**

A subdivision within 100 feet of a public water system must be connected to the public water system. The director may waive this requirement.

If a subdivision is to be served by a public water system:

- *approval of the water system plans by the director of the Water and Wastewater Utility is required;*
- *installation of the water system must comply with the requirements of this title and the Utilities Criteria Manual; and*
- *water lines to serve each lot must be installed before a lot may be occupied.*

Source: Section 13-2-476; Ord. 990225-70; Ord. 031211-11.

- **§ 30-2-192 – Wastewater Lines (Austin/Travis County Subdivision)**

A subdivision within 100 feet of a public wastewater system must be connected to the public wastewater system. In the extraterritorial jurisdiction, the director may waive this requirement. In the zoning jurisdiction, this requirement may be waived under Section 25-9-4 (Connection To Organized Wastewater System Required).

If a subdivision is to be served by a public wastewater system or community disposal system, wastewater lines to serve each lot must be installed before a lot may be occupied.

Source: Section 13-2-475; Ord. 990225-70; Ord. 031211-11.

- **§ 25-9-412 Reclaimed Water Connection Requirements.**

(A) A small development project with a property boundary located within 250 feet in horizontal distance of a reclaimed water line, measured based on the closest practicable access route, shall connect to a reclaimed water line and use reclaimed water for irrigation, cooling, toilet flushing, and other significant non-potable water uses identified in the water balance calculator.

(B) A large development project with a property boundary located within 500 feet in horizontal distance of a reclaimed water line, measured based on the closest practicable access route, shall connect to a reclaimed water line and use reclaimed water for irrigation, cooling, toilet flushing, and other significant non-potable water uses identified in the water balance calculator.

- **§ 6-4-11(E) Mandatory Reclaimed Water Connection**

Except for municipal uses associated with law enforcement or public health and safety, all new commercial developments or redevelopments located within 250 feet of a reclaimed water distribution line are required to obtain and utilize permitted connections to reclaimed water for irrigation, cooling, and other significant non-potable water uses.

- **§ 15-9-9 – Criteria Manuals**

The Utilities Criteria Manual and the Water and Wastewater Design Criteria Manual apply to utility service provided under the Code.

Source: Ord. 040805-02.

- **§ 15-9-152 – Design and Installation Guidelines**

The directors of the Electric Utility and the Water Utility shall adopt design and installation guidelines related to a customer's installation and the City's service connection.

A person authorized to install a customer's installation or the City electric utility equipment or facilities shall comply with the City's "Utilities Criteria Manual."

A person authorized to install a customer's installation or the City's water utility equipment or facilities shall comply with the City's Utilities Criteria Manual, standards, and specifications.

Source: 2003 Code Sections 15-9-211(A) and (B); 1992 Code Sections 18-4-300(A) and (B); Ord. 040805-02; Ord. No. [20180524-006](#), Pt. 8, 6-4-18.

- **TCEQ Chapter §291.93. Adequacy of Water Utility Service.**

*Sufficiency of service. Each retail public utility which provides water service shall **plan**, furnish, **operate**, and **maintain** production, treatment, storage, transmission, and distribution facilities of sufficient size and capacity to provide a continuous and adequate supply of water for all reasonable consumer uses.*

- **TCEQ Chapter §291.94. Adequacy of Sewer Service.**

*Sufficiency of service. Each retail public utility shall **plan**, furnish, **operate**, and **maintain** collection, treatment, and disposal facilities to collect, treat and dispose of waterborne human waste and waste from domestic activities such as washing, bathing, and food preparation. These facilities must be of sufficient size to meet the minimum design criteria for wastewater facilities of the commission for all normal demands for service and provide a reasonable reserve for emergencies.*

In addition, this specific project does meet with the following Utility Criteria Manual sections 2.2.0 thru 2.9.

In accordance with section 15-9-276 of City Code, the project will need dedicated and recorded water/wastewater or reclaimed water easements.

- **§217.321. Safety Design of a Wastewater Treatment Facility.**

*(b) Occupational **safety and health hazards, and risks to workers and the public**, must be addressed in the design of collection system and wastewater treatment facility equipment and processes.*

- **§291.95. Standards of Construction.**

In determining standard practice, the commission will be guided by the provisions of the American Water Works Association, and such other codes and standards that are generally accepted by the industry, except as modified by this commission, or municipal regulations within their jurisdiction. Each system shall construct, install, operate, and maintain its plant, structures, equipment, and lines in accordance with these standards, and in such manner to best accommodate the public, and to prevent interference with service furnished by other retail public utilities insofar as practical.

RESPONSES TO ALL OF THE RED LINED COMMENTS/QUESTIONS MUST BE MADE IN A DIFFERENT COLOR ON THE PLAN SET WITH AN EXPLANATION OF HOW AW COMMENTS/QUESTIONS HAVE BEEN ADDRESSED.

PLEASE INDICATE IF THE PROJECT WILL BE SUBMITTED TO AULCC FOR REVIEW AND IF SO, INCLUDE ROW ID# and UCC PERMIT # ON THE UTILITY PLAN SHEET.

Update 0 – 06/05/2026.

City Arborist Review – Dillon Olsen – (512) 974-2515 – dillon.olsen@austintexas.gov
--

STANDARD PRESERVATION REQUIREMENTS

Transplant Proposals:

CA01 – Current Status: Pending

- U0: Transplants

Heritage Tree #5001 is proposed to be transplanted on site.

Demonstrate that these trees cannot be preserved in place by providing alternative layouts in a buildability exhibit. Demonstrate that all associated site improvements impacting the transplanted tree, in its final location, will meet preservation criteria (see CA10).

If demonstrated that meeting preservation criteria for Heritage Tree #5001 in its existing location is not feasible, the following criteria must be met:

- Provide a tree transplant feasibility report prepared by a certified arborist. The report must include:
 - Condition and suitability of trees proposed for transplant;
 - Excavation and root ball stabilization method;
 - Transport method;
 - Transport schedule;
 - Tree storage methods if any;
 - Remedial tree care plan
- A 5-year Tree Care Plan by a certified arborist. (to be included within the Landscape Plans)
- Fiscal surety must be posted for the tree proposed to be transplanted. Fiscal will be posted in the amount of mitigation that would be owed for the tree.
- Fiscal surety is not eligible for release until five years after the date the transplant occurred.

Reference: ECM 3.5.2.B.5

Demolition:

CA02 – Current Status: Pending

- U0: Revise the tree protection fencing layout on the Demolition Plan to account for demolition work within the area encompassed by the tree fencing. Add the following note to the Existing Conditions/Demolition Plan:
 - Tree protection fencing is required for all trees within the limits of destruction on site before demolition occurs. Where fencing cannot be placed to protect the extent of the CRZ with natural ground cover, provide an 8" layer of organic hardwood mulch outside of the fencing.
 - Trunk armor to be added to avoid mechanical impacts. Strap 2x4 or thicker lumber (to match height of building) securely around tree trunk, buttress roots, and root flare, if fencing is within 5 feet or less of the trunk.
 - If pruning is necessary during demolition, it should take place prior to the start of the demolition process. It must be performed by a qualified arborist and no more than 25% is permitted.

Reference: ECM 3.6.1

CA03 – Current Status: Pending

- U0: When demolishing existing structures, removing utilities, and/or removing flatwork within the CRZs of trees 8" or greater in diameter, **add callouts** for trees to be preserved specifying low impact excavation methods.

Reference: ECM 3.5.2.B.2

Erosion & Sediment Control Plan:

CA04 – Current Status: Pending

- U0: Show trees proposed for removal with a dashed circle on the Erosion & Sedimentation Control Plan, along with the proposed layout, and note the removal graphic in the plan legend, and removals in the tree list.

Reference: ECM 3.3.2.D

Tree Protection:

CA05 – Current Status: Pending

- U0: Show the specific locations of tree protection fencing for all regulated trees (8" in diameter or greater) to be preserved within and adjacent to the limits of construction on the Demolition and Erosion & Sedimentation Control Plans (including trees proposed for transplant). Add tree protection to Tree #5012.

Reference: ECM 3.6.1

CA06 – Current Status: Pending

- U0: Update tree protection fencing to meet the following:
 1. Extend all tree protection fencing to fully enclose as much of the Full CRZ as possible.
 2. When fencing cannot be installed around the Full CRZ:
 - (a) Install fencing up to existing or proposed impacts and add 8" of hardwood mulch outside of the fence to the Full CRZ.
 - (b) Call outs are needed for all trees when fencing is located 5 feet or less from the trunk. Call outs must state: "Trunk Wrapping: 2x4x6 or greater size lumber shall be strapped vertically to the tree and 8" of hardwood mulch shall be applied within the Full CRZ." Per standard [detail 610S-4](#) of the ECM.

Reference: ECM 3.6.1

CA07 – Current Status: Pending

- U0: Tree protection fencing cannot be shown to conflict with demolition, grading or proposed construction. The intent of the tree protection fencing is to be installed prior to demolition/ construction and remain in place until project completion. Fencing must be continuous and create a closed, inaccessible area of root zone protection. If a phased tree protection plan is needed, based on demolition and construction activities, provide a tree protection plan for demolition on the demolition plan and a second one for proposed construction on the ESC sheets. Proposed grading is shown inside of tree protection fencing for Trees #5032 and #5038 (both are invasive species). Either grading should be modified to be outside of the fencing, or fencing should be modified (no mitigation is required for impacts to these trees).

CA08 – Current Status: Pending

- U0: For ROW trees, show tree protection fencing or trunk planking strapped vertically to the tree and 8" of hardwood mulch applied to all unfenced areas of the root zone.

CA09 – Current Status: Pending

- U0: Mulch Specifications
If access within the Half Critical Root Zone is required, install decking (3/4-inch plywood) over 8 inches of mulch to provide additional protection against soil compaction during construction. Provide graphic (cross-hatching) with callouts to illustrate specific area(s) where alternative mulch & decking will occur.

Reference: ECM 3.6.1.C

Tree Preservation Criteria:

CA10 – Current Status: Pending

- U0: Trees to be preserved must meet the following criteria:
 1. At least fifty percent of the total area (square footage) of the Critical Root Zone must be preserved at natural grade, with natural ground cover.
 2. The entirety of the Half CRZ must be protected, with the exception that cut or fill of 4" or less is allowed within the Half CRZ.
 3. No cut or fill is allowed within the Quarter CRZ.

Reference: ECM 3.5.2.A.1

CA11 – Current Status: Pending

- U0: Demonstrate what the required over-build(s) will be for the proposed building construction and proposed curbs. This information is necessary to determine where the actual line(s)-of-impact will be in relation to the Half CRZs of Trees #5002 and #5003, and Heritage Tree #5000, shown to be preserved.

Reference: ECM 3.5.2.A.3

CA12 – Current Status: Pending

- U0: Proposed grading, stormwater, and rock berm, impacts to Trees #5009 and #5010 on the adjacent property do not meet tree preservation criteria. These trees cannot be removed without obtaining explicit permission from the neighboring property owner. Provide a letter from the owner granting permission to remove and mitigate for their tree. If the owner does not grant permission or cannot be contacted, then modify the plans to meet tree preservation criteria. Mitigation must be provided if the tree is removed (see CA15).

Reference: ECM 3.5.2

Sidewalk:**CA13 – Current Status: Pending**

- U0: A sidewalk is proposed within the Quarter and Half CRZs of Heritage Tree #5000 (24-inch Red Oak). Additionally, the installation of a sidewalk typically requires excavation around the sidewalk farther than shown by its footprint on the plan. In such a case, the line of impact on the CRZ includes a greater area than is shown on the plan.

Revise the sidewalk construction/layout to meet CRZ preservation criteria per CA10.

An elevated sidewalk appears to be the best method for meeting preservation criteria. Provide a detail that demonstrates how the elevated sidewalk will meet the following requirements:

1. An air gap or void with a minimum height of 4 inches between bottom of sidewalk/material and natural grade.
2. The soil beneath the void spaces is preserved at natural grade.
3. Low impact excavation must occur when piers are proposed in the Half CRZ to avoid damaging significant roots at least 1.5 inches in diameter, or greater. The pier locations must be adjustable to allow shifting in the field if significant roots are present where the piers are proposed.
4. Holes excavated within the Half CRZ(s) shall be lined with a non-leaching barrier.

Reference: ECM 3.5.2

CA14 – Current Status: Pending

- U0: A sidewalk is proposed within the CRZs of Trees #5004-5008 that does not meet CRZ preservation criteria (see CA10). The sidewalk may be realigned for a more direct layout, with mitigation provided for these trees.

Crown Preservation:**CA15 – Current Status: Pending**

U0: Demonstrate how the proposed construction (e.g. building, grading, detention pond, etc) including the installation of scaffolding, does not require removal of more than 25% of the crowns of Heritage Trees #5000 and #5001.

Provide a tree crown assessment for each tree by a qualified 3rd party arborist in PDF format. The assessment must include:

- The tree number, size, and species of tree(s).
- Photos of the tree(s) include:
 - Tree number

- Entire tree from root to top of crown
- Identifies the exact location of major pruning cuts, and
- Estimates the overall crown percentage to be removed.

Reference: ECM 3.5.2.A.2

TREE MITIGATION

CA16 – Current Status: Pending

- U0: Proposed development does not meet preservation criteria for Trees #5009 and #5010 (Grading, stormwater, rock berm), and #5004-5008 (grading, curb, sidewalk). Show these trees to be mitigated in the plans and include them in mitigation calculations.

Revise the Tree Mitigation Plan compliant with Chapter 25-8, Subchapter B, Article 1, Division 2 of the City of Austin Land Development Code and Section 3 of the City of Austin Environmental Criteria Manual. Planting new trees or the preservation of unregulated trees are the primary forms of mitigation. Alternative mitigation may be approved by the City Arborist when a site is unsuitable for planting.

Reference: ECM 3.5.4

Calculating Mitigation:

CA17 – Current Status: Pending

- U0: Tree mitigation must be provided (at minimum) at the following rates:
 - Heritage trees: 300%
 - 19 inches and greater, ECM Appendix F trees: 100%
 - 8 to 18.9 inches, ECM Appendix F trees: 50%
 - 19 inches and greater, all other trees: 50%
 - 8 to 18.9 inches, all other trees: 25%

Note: No mitigation is required for the removal of non-native invasive species.

Reference: ECM 3.5.4.A.1

Forms of Mitigation:

CA18 – Current Status: Pending

- U0: Label all mitigation trees on the landscape plan and provide a table showing allocation of replacement inches between landscape and tree ordinance requirements. Additionally, only the surplus inches (beyond minimum caliper) of a street yard, parking lot tree and buffer tree may be counted towards mitigation, not the full amount of inches planted. (e.g., 4" tree planted = 1.5 inches required for street yard, 2.5 inches remaining towards mitigation). Recalculate the mitigation planting and provide additional inches for mitigation. Additional review and comments are pending.

CA19 – Current Status: Pending

- U0: Qualifying Species - Significant Shade Providing Trees
No less than 75% of the total caliper inches of mitigation trees required must be represented by significant shade trees located in the ECM Appendix F. The remaining 25% of total caliper inches may be represented by a mixture of the ECM Appendix F tree species.
All trees selected must be suitable for the environment of the immediate planting site (see ECM Appendix F for specific categorization such as tree, soil, site, or regulatory qualities). Eligible replacement tree species are listed in Environmental Criteria Manual Appendix F. The City Arborist may approve species not listed in Appendix F for mitigation credit.

Reference: ECM 3.5.4 2. B.1.b

CA20 – Current Status: Pending

- U0: Qualifying Species - Diversity
 1. When twenty or more inches of replacement trees are planted on a site they must be selected from at least two species.
 2. When one hundred or more inches of replacement trees are planted on a site they must be selected from at least five species, with no single species representing more than fifty percent of the total caliper of the required mitigation.

All trees selected must be suitable for the environment of the immediate planting site (see ECM Appendix F for specific categorization such as tree, soil, site, or regulatory qualities).

Reference: ECM 3.5.4 2. B.1.b

Urban Forest Accounting:

CA21 – Current Status: Pending

- U0: Provide a chart listing the following mitigation information as formatted below on the landscape sheets. Update totals with subsequent plan changes.

Surveyed:

- Total Appendix F tree inches surveyed;
- Heritage tree inches surveyed;
- Non-Appendix F tree inches surveyed; (includes invasive and Non-App F)
- Invasive tree inches surveyed;

Removed:

- Total Appendix F inches removed;
- Heritage Tree inches removed;
- Total Non-Appendix F inches removed; (includes invasive and Non-App F)
- Invasive inches removed;
- Total Dead, Diseased, or Imminent Hazard (DDI) inches removed;
- DDI Appendix F inches removed;
- DDI Heritage tree inches removed;
- DDI Non-Appendix F inches removed;
- DDI Invasive inches removed;

Mitigation:

- Total mitigation replacement inches planted;
- Total replacement inches planted on site (private trees);
- Total replacement ROW inches planted;
- Private inches owed to Urban Forest Replenishment Fund (UFRF)
- Public inches owed to UFRF
- Total non-mitigation inches planted on site

Reference: ECM 3.5.4

GENERAL NOTES

CA22 – Current Status: Pending

- U0: Remove ECM Appendix P-2 from the plans (sheets 5 and 44), and replace it with the modified tree & natural area protection standard plan note found in [ECM section 3.6.2](#). See [ECM 3.6.1](#) for additional information and criteria.

OWB1– Current Status: Pending

- U0: The 2nd portion of the water benchmarking application has not been completed- please use the following link to answer the questions on page 9 of 9: [Waterbenchmarking_dashboard](#)

OWB2– Current Status: Pending

- U0: Applicant stated the Gross Floor Area may change as building design changes. As of right now, the GFA listed on the benchmarking application does not match the GFA listed on the site plan

OWB3– Current Status: Pending

- U0: The Building Coverage listed on the site plan is inconsistent with the benchmarking application- please ensure these values match

OWB4– Current Status: Pending

- U0: If the Building Coverage value changes per comment OWB3, please update the “Other Impervious Area” input on the benchmarking application

OWB5– Current Status: Pending

- U0: The Total Irrigated Landscaped Area exceeds the amount of pervious area available on site for landscape irrigation. Please confirm the inputs are correct

OWB6– Current Status: Pending

- U0: If the Gross Floor Area value is updated per comment OWB2, please update the “Building information” section of the benchmarking application

OWB7– Current Status: Pending

- U0: The “Eating and Drinking-Restaurant” GFA listed on the benchmarking application is 6,000sf- however, on the site plan is listed as 9,776sf- which is correct? Please update the benchmarking application if necessary

OWB8– Current Status: Pending

- U0: The Building Coverage listed on the site plan is inconsistent with the benchmarking application- please ensure these values match

OWB9– Current Status: Pending

- U0: If the benchmarking application needs updating, please use the following link: [Water Benchmarking Survey](#)

Case Manager Review – Jim Gobel (512) 978-6414 - jim.gobel@austintexas.gov
--

Clarification of Reviewer Comments

CM 1 – Current Status: Informational

- U0: If there is any confusion on a specific reviewer's comments, please email that reviewer directly and copy the case manager. The case manager can facilitate a meeting if required.

Post-Review Cycle Meeting

CM 2 – Current Status: Informational

- U0: Applicants are strongly encouraged to meet with reviewers after the U2 or U3 review to ensure the project is completed in a timely manner. Meetings are conducted remotely via Microsoft Teams; individual review comments will not be cleared during this time. Please get in touch with your Case Manager to schedule this meeting.

Legal Documents

CM 3 – Current Status: Informational

- U0: Please confirm with each reviewer whether any legal documents are required, including easements, license agreements, UDAs, restrictive covenants, etc. If so, ensure that a placeholder is included in the plan set for each corresponding document; the recordation number must be filled in after each document is recorded.

NOTE: Please copy the case manager with any correspondence regarding legal documents.

CM 4 – Current Status: Informational

- U0: A license agreement is required for any vertical improvements (e.g. trees, furniture, irrigation, or other structures) in the right-of-way. Please visit <http://austintexas.gov/page/land-management> for more information. Begin this process as soon as possible as it can take considerable time. If a "streetscape" is required, be advised to present final set of plans to Case Manager to distribute for signatures from AFD, AW, and IW to then forward to Land Management to record "streetscape" License Agreement. Currently, this process with LM is approximately a 30-day turnaround.

Housing Certification letter updates

CM 5 – Current Status: Informational

- U0: Please let the case manager know if you have updated your housing certification letter to increase or decrease your participation in a City-sponsored program.

Fiscal Posting/Fees

CM 6 – Current Status: Pending

- U0: Please inform the case manager when fiscal is posted, or fees are paid. Provide a fiscal surety receipt from the Fiscal Surety Office as documentation for posting.

NOTE: If a Landscape Inspection Fee is required by Environmental, please be sure to go to Intake to have the fee added to your file so that you can pay the fee through the Austin Build Connect (ABC) portal.

Signature Process

CM 7 – Current Status: Pending

- U0: When all comments are cleared, collect signatures/authorizations from reviewers external to the City of Austin, if required. Then coordinate with the Case Manager to circulate the final plan set for City of Austin required signatures. Please allow up to 5 business days for signatures to be completed.
NOTE: Any changes to the plan set following the final submittal will require the Case Manager to restart the process of collecting signatures.

Tax Certificate

CM 8 – Current Status: Pending

- U0: A new tax certificate showing all taxes paid through the most current year: 2026 is required prior to site development permit issuance.

CM 9 – Current Status: Rejected.

- U0: Please check your page numbers. Your sheet index references 52 sheets, but the plans have 54 sheets.

CM 10 – Current Status: Pending

- U0: Show the formal submittal date on the cover sheet as **MAY 18, 2026**. Note, this is the same date as the application date in the approval block.

CM 11 – Current Status: Rejected

- U0: The name and address of the applicant on the plans do not match the application. Please correct either the plans or the application so that the name and address match.

CM 12 – Current Status: Pending

- U0: Provide a blank 1" x 1" space in the lower right-hand corner on each sheet for batch stamping at time of permitting. Note: No signature blocks should be within the space.

CM 13 – Current Status: Pending

- U0: Add the following approval block to lower right of coversheet only:

SITE PLAN APPROVAL

CASE NUMBER: **SP-2026-0136C** APPLICATION DATE: **MAY 18, 2026**

APPROVED ON _____ ☐ ADMINISTRATIVELY ☐ BY COMMISSION

UNDER SECTION ☐112 ☐142 OF CHAPTER 25-5 OF THE CITY OF AUSTIN CODE

EXPIRATION DATE (LDC 25-5-81) _____ CASE MANAGER **JIM GOBEL**

AUSTIN DEVELOPMENT SERVICES

RELEASED FOR GENERAL COMPLIANCE _____ ZONING _____

APPROVAL STAMPS:

CM 14 – Current Status: Informational

- U0: During the review cycle, if the ownership changes, please make sure that the new owner information is entered into the system to avoid any permit issuance delays. We will also need a new warranty deed showing the new owner as well as a letter from the new owner authorizing the applicant to act on their behalf.

AW Reclaim and Reuse Review – Dalila Loiacomo (512) 972-1050 -
dalila.loiacomo@austintexas.gov

This project is required to implement Onsite Water Reuse Per [Chapter 15-13 of City Code](#). If there are any questions about the applicability of this requirement, please contact AW_Onsitereuse@austintexas.gov as soon as possible to prevent any delays to project permitting.

Please visit the OWRS program [website](#), where you will find information about the permitting process and requirements to install an OWRS. Please note:

- **OWRS require an independent OWRS Permit** in addition to showing the OWRS system components on Site Plans and Building Plans.
- **Building Permits will not be approved until the OWRS Permit Application is approved.**

AWRR1 – Current Status: Pending

- **U0: Water Balance Calculator (WBC).** Request the most current version of the WBC via email at AW_Onsitereuse@austintexas.gov. Please return filled out WBC via email once it is completed. *TIPS:*
 - *Make sure you are using the current version of WBC.*
 - *Make sure the building coverage and gross floor area match what is reported in the Site Plan Data Table on the Site Plan sheet.*
 - *Make sure you have no red text anywhere in the WBC which indicates an error.*

AWRR2 – Current Status: Pending

- **U0:** Please include the following items in the Austin Water General Notes Sheet:
 2. **The dedicated back up meter to OWRS.** This meter must be included in the Meter Notice Table as “Potable Back-up to OWRS (NP Meter)”.
 3. **OWRS Meter Demand Sheet.** The required dedicated OWRS City meter must be sized based on the fixture and flow demands served by the OWRS. Request the Meter Demand spreadsheet via email (AW_Onsitereuse@austintexas.gov). The spreadsheet must be filled out and included in the Austin Water Notes sheet of the project’s Site Plan sheet set. Most projects will realize a reduction in their water and wastewater impact fees since there are no service units associated with the OWRS make up meter and the potable water meter only needs to be sized to serve the project’s potable fixtures. *TIP: make sure the peak flows on your meter demand sheet correspond with the peak flows on your Fire Domestic and Irrigation Demand Data Table and the peak flows listed for your meter in the Meter Notice Table on the AW General Notes Sheet.*

AWRR3 – Current Status: Pending

U0: Please include the OWRS components in the Overall Utility Plan sheets. At a minimum, the sheets must show:

1. Dedicated City meter (labeled “Potable Back-up to OWRS (NP Meter)”)
2. Make up water line from Back-up OWRS to OWRS meter to the OWRS cistern (labeled as “OWRS back-up”).
3. Containment Reduced Pressure Principle Backflow Prevention Device (RPZ) immediately downstream of the point of connection with all City water meters serving the property.
4. Distribution line from OWRS collection tank to end uses.
5. Location of the OWRS collection tank. If tank is indoors, note that.
6. Please include the following note at collection cistern: “For OWRS details, including treatment, monitoring, controls, please refer to OWRS permit and OWRS sheets in building plans”

AWRR4 – Current Status: Pending

- **U0: Storm drain sheet:** Overflow connections to the storm drain system with air gap (or sanitary drains for graywater systems).

AWRR5 Current Status: Pending

- **U0:** A meeting with the AW-OWRS team is required for Developments with a Gross Floor Area larger than 250,000 square feet. If OWRS staff has not already reached out to you to schedule a meeting, please email AW_Onsitereuse@austintexas.gov to schedule the mandatory meeting. If you have already met with OWRS staff, please note the date of the meeting.

AWRR6 – Current Status: Pending

- **U0: Cross connection AMOC.** Buildings with OWRS will be required to undergo initial and periodic cross-connection testing to ensure separation between the potable and non-potable water systems. A typical two-sided cross-connection test involves draining both the potable water system and the non-potable water system in a building and then re-pressurizing these systems one at a time to ensure there is no interconnection between the two systems. This requires a building to be without water services for a substantial amount of time. Having an Alternate Method of Compliance (AMOC) approved during the plan review process can eliminate the need to shut down a building during a cross-connection test. Please see our [CCT Guidance](#) for information on obtaining a CCT AMOC.

AWRR7 – Current Status: Pending

- **U0:** Please confirm that this project does not have a concurrent PR review. If it does, please provide the PR number to avoid PR permitting delays.

AWRR8 – Current Status: FYI

- **U0:** Project with OWRS are required to obtain an OWRS Permit. To begin this process submit an [OWRS Permit Application](#) – Go to the [AB+C Portal](#) to submit OWRS Permit Application. This may happen at any time in the project, and does not need to be complete before your Site Plan can be approved. However, **the Building Permit will not be approved until the OWRS Permit Application is approved.**

END OF MASTER COMMENT REPORT

Comment Resolution Process:

You can submit a Comment Resolution Request if:

1. You have identified two or more comments in your Master Comment Report that conflict with each other; and
2. You do not believe that the comments can be satisfied.

Comment Resolution Requests can only be submitted and resolved between review cycles. They cannot be submitted while the site plan is in review. Use the [Comment Resolution Request Web Form](#) to submit your request.

Questions or Concerns? Contact Us:

If you have any questions or concerns or if you require more information about this report, please do not hesitate to contact your Case Manager at the email address listed at the top of this report or by writing to the City of Austin, Development Services Department, P.O. Box 1088, Austin, Texas 78767.
